

Future Project Outlook

<u>Upcoming Projects</u>			
Tracs	Route	Project Name	Type of Work
T0247	Flagstaff	Fourth St. / Cedar Ave. / Lockett Rd	Construct Roundabout
T0251	Cottonwood	Blowout Wash Bridge	Bridge Deck Rehabilitation
F0333	Statewide	Wrong Way Signs (Phase V)	Wrong Way Do Not Enter Signs
F0308	I-15	Black Rock TI	Bridge Rehabilitation
F0362	I-17	Airport Rd Ti	Bridge Replacement
F0207	I-17	SB County Line to McConnell Bridge	Pavement Rehabilitation
F0107	I-40	A-I Mountain TI.	Bridge Replacement (Bid Opened)
F0281	I-40	Transwestern - Cosnino Rd.	Variable Speed Limit Signs & Operations (On-hold)
F0333	US-89	Wash, Moenkopi & Five Mile Wash Bridges	Bridge Rehabilitations
F0139	SR-260	Lion Springs Section	Rural Corridor Reconstruction
H8245	SR-260	Rim Rd - Gibson Rd, Segment 1 & 2	Shoulder Widening (Advertised)
F0351	SR-87	Various Locations	HSIP Tree Removal
F0277	SR-99	Canyon Diablo Bridge	Minor Bridge Repairs and Scour Retrofit
H8778	SR-89A	Pumphouse Wash Bridge	Bridge Rehabilitation (Bid Rejected)
H8907	SR-89A	Erosion & Sediment Control	Alleviate Slope Erosion (Bid Rejected)
F0154	SR-89A	MP 375.1 & 389.2	Rockfall Mitigation (Bid Rejected)
F0296	SR-89A	SR-89A to I-40B Milton Rd.	Pavement Preservation

NORTHCENTRAL DISTRICT CONTACTS

Audra Merrick, District Engineer	928-779-7596
Brenden Foley, Assistant District Engineer (Construction & Development)	928-779-7591
Chad Auker, Assistant District Engineer (Maintenance)	928-779-7551
Nate Reisner, Transportation Engineer	928-779-7545
Deborah Miller, Community Relations	(c)928-777-5986
Doug Carroll, Community Relations	(c)928-707-9370
Vern Dumbeck, Permits Supervisor	928-779-7529
Sheri Chesser, Maint. Superintendent	928-779-7552
Thomas Eckler, Jr., Maint. Superintendent	928-779-7531

Maintenance Projects "Current/Upcoming"

Route	Type of Work	Location	Unit
I40	Crack Seal	MP 205-229.9	5151
I40	Crack Seal	MP 146-156	5152
US 89	Spot Overlays	MP 275 - 295	5153
SR 89A	Crack Seal	MP 357 - 375	5154
SR 98	Crack Seal	MP 298 - 310	5155
I-15	Flush	MP 21.2 - 29.4	5156
SR260	Crack Seal	MP 270-302	5160
SR 260	Crack Seal	MP 220 - 240	5161
SR87	Flush	MP 3445-361	5162



NORTHCENTRAL DISTRICT 2nd QUARTER STATUS REPORT


**October 2021~December 2021
Fiscal Year 2022**

**Audra Merrick
District Engineer**

**District Office: 928-774-1491
Fax: 928-779-5905**

www.azdot.gov

**Northcentral District Office
1959 S. Woodlands Blvd.
Flagstaff, AZ 86001**

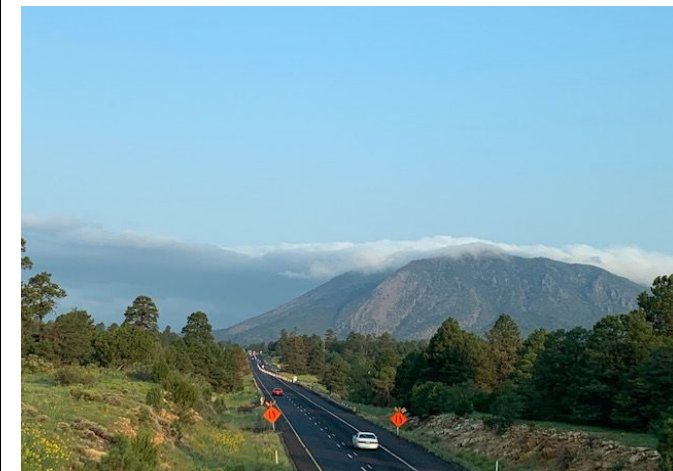

CURRENT PROJECTS

Construction A (Flagstaff)

UNIT 4352 - Vacant (Sr. RE), Brent Allman (RE)
928-714-2290

Route / Project Name	I-17 / McGuireville RA to Flagstaff (F0420)
Type of Work	ITS Infrastructure
% Complete (Start of Quarter) / Bid Amount	0% / \$7,998,372
Contractor	William Charles Construction Company

Route / Project Name	I-40 / Winona TI (F0108)
Type of Work	Bridge Deck Replacement
% Complete (Start of Quarter) / Bid Amount	100% / \$3,881,894
Contractor	FNF Construction, Inc.

Route / Project Name	I-40 / I-17 to Walnut Canyon Road (F0185)
Type of Work	Pavement Preservation
% Complete (Start of Quarter) / Bid Amount	54% / \$16,434,861
Contractor	FNF Construction, Inc.

Route / Project Name	SR-89A / SR-89A & SR-179 Sedona Modernization (F0206)
Type of Work	Minor Pavement Preservation
% Complete (Start of Quarter) / Bid Amount	0% / \$655,860
Contractor	Asphalt Paving & Supply, Inc.



CURRENT PROJECTS

Construction B (Flagstaff)

UNIT 4353 - Cordell Yazzie (RE)
928-714-2225

Route / Project Name	I-15 / Virgin River Bridge No. 1 (H8760)
Type of Work	Bridge Replacement
% Complete (Start of Quarter) / Bid Amount	35% / \$55,994,446 (CMAR)
Contractor	Kiewit Infrastructure West Co.

Route / Project Name	I-40 / West Flagstaff TI (H8777)
Type of Work	Bridge Replacement
% Complete (Start of Quarter) / Bid Amount	74% / \$6,489,937
Contractor	Sundt Construction, Inc.

Route / Project Name	B-40 / Rio De Flag Bridge (H8905)
Type of Work	Bridge Replacement
% Complete (Start of Quarter) / Bid Amount	100% / \$4,942,893
Contractor	FNF Construction, Inc.

Route / Project Name	SR-179 / I-17 to Red Rock Vista (F0167)
Type of Work	Pavement Preservation
% Complete (Start of Quarter) / Bid Amount	59% / \$4,249,000
Contractor	Sunland Asphalt & Construction,



CURRENT PROJECTS

Construction C (Payson)

UNIT 4355 - Vacant (Sr. RE),
Teague (Consultant RE) 623-640-8304

Route / Project Name	I-40 / Leupp Rd TI (F0153)
Type of Work	Bridge Deck Rehabilitation
% Complete (Start of Quarter) / Bid Amount	78% / \$2,090,213
Contractor	Pulice Construction, Inc.

Route / Project Name	SR-87 / Pine Creek to SR-260 (H8508)
Type of Work	Shoulder Widening
% Complete (Start of Quarter) / Bid Amount	38% / \$4,747,474
Contractor	Fann Contracting, Inc.

Route / Project Name	I-40 / Babbitt Tank WB & Buffalo Range EB (H8928)
Type of Work	Bridge Decks Rehabilitation
% Complete (Start of Quarter) / Bid Amount	100% / \$3,472,182
Contractor	Vastco, Inc.

Route / Project Name	I-17 / Verde River Bridges
Type of Work	Construct Scour Retrofit
% Complete (Start of Quarter) / Bid Amount	6% / \$1,868,403
Contractor	Vastco, Inc.

