

Northwest District

Prescott ~ Kingman
Lake Havasu~Bullhead City
Chino Valley~Prescott Valley
Dewey-Humboldt~Mayer
Cordes Junction~Ash Fork~Seligman
Black Canyon City~Wickenburg~Wikieup

QUARTERLY STATUS REPORT

**July-September
2025**

Anthony Brozich
District Administrator

1109 E. Commerce Dr.
Prescott, AZ 86305

Phone: 928.777.5861
Fax: 602.239.6219

www.azdot.gov

Revised 07/01/2025

Prescott Office Contacts 1109 E. Commerce Dr. Prescott, AZ 86305

Andrew Roth Assist Dist Engineer Construction	928.777.5869
Nicole Underwood Community Relations Project Mgr Yavapai County Area	480.601.1575
Gabe Alvarado Hwy Operations Superintendent Yavapai County Area	928.681.6025 928.777.5868
John Casey Sr Transportation Engineer Development	928.777.5865
Debbie Montgomery Construction Office Tech III	928.777.5895
Richard Perez District Permits Supervisor	928.777.5874
Troy Keating Permit Technician	928.777.5875
Kaili Calasso Permit Technician	928.777.5930
Jason Elmer District Environmental Coordinator	928.777.5966
Colleen Spence Admin Services Officer 1	928.777.5881



FOR CURRENT TRAFFIC ALERTS
Phone 5-1-1 or on the web @
www.az511.gov


Kingman Office Contacts 3660 E. Andy Devine Ave. Kingman, AZ 86401

Todd Steinberger Assist Dist Engineer Maintenance/Permits	928.681.6039
Michele E. Beggs Community Relations Project Mgr Mohave County Area	928.566.5052
Nathan Escoffier Hwy Operations Superintendent Mohave County Area	928.681.6048
Sam Massey Development TES	928.681.6019
Raelyn Lott Permits Technician	928.681.6017
Jose Duran-Ibarra Permit Technician	928.681.6038

Maintenance Projects “Current/Upcoming”

<u>PROJECT</u>	<u>DATES</u>
SR 69 MP 2-4 Pavement Repairs	July 2025
SR 89 MP 320-328 Fog seal	July 2025
SR 169 MP 2-4 Drainage Repair	July 2025
US 93 MP 131.8 Erosion/Drainage Repair Box Canyon	July 2025
I-40, MP 28 Pavement Repairs	July 2025
SR 95 Spur Pavement/Drainage Repairs	July 2025

Northwest District Maintenance Boundaries

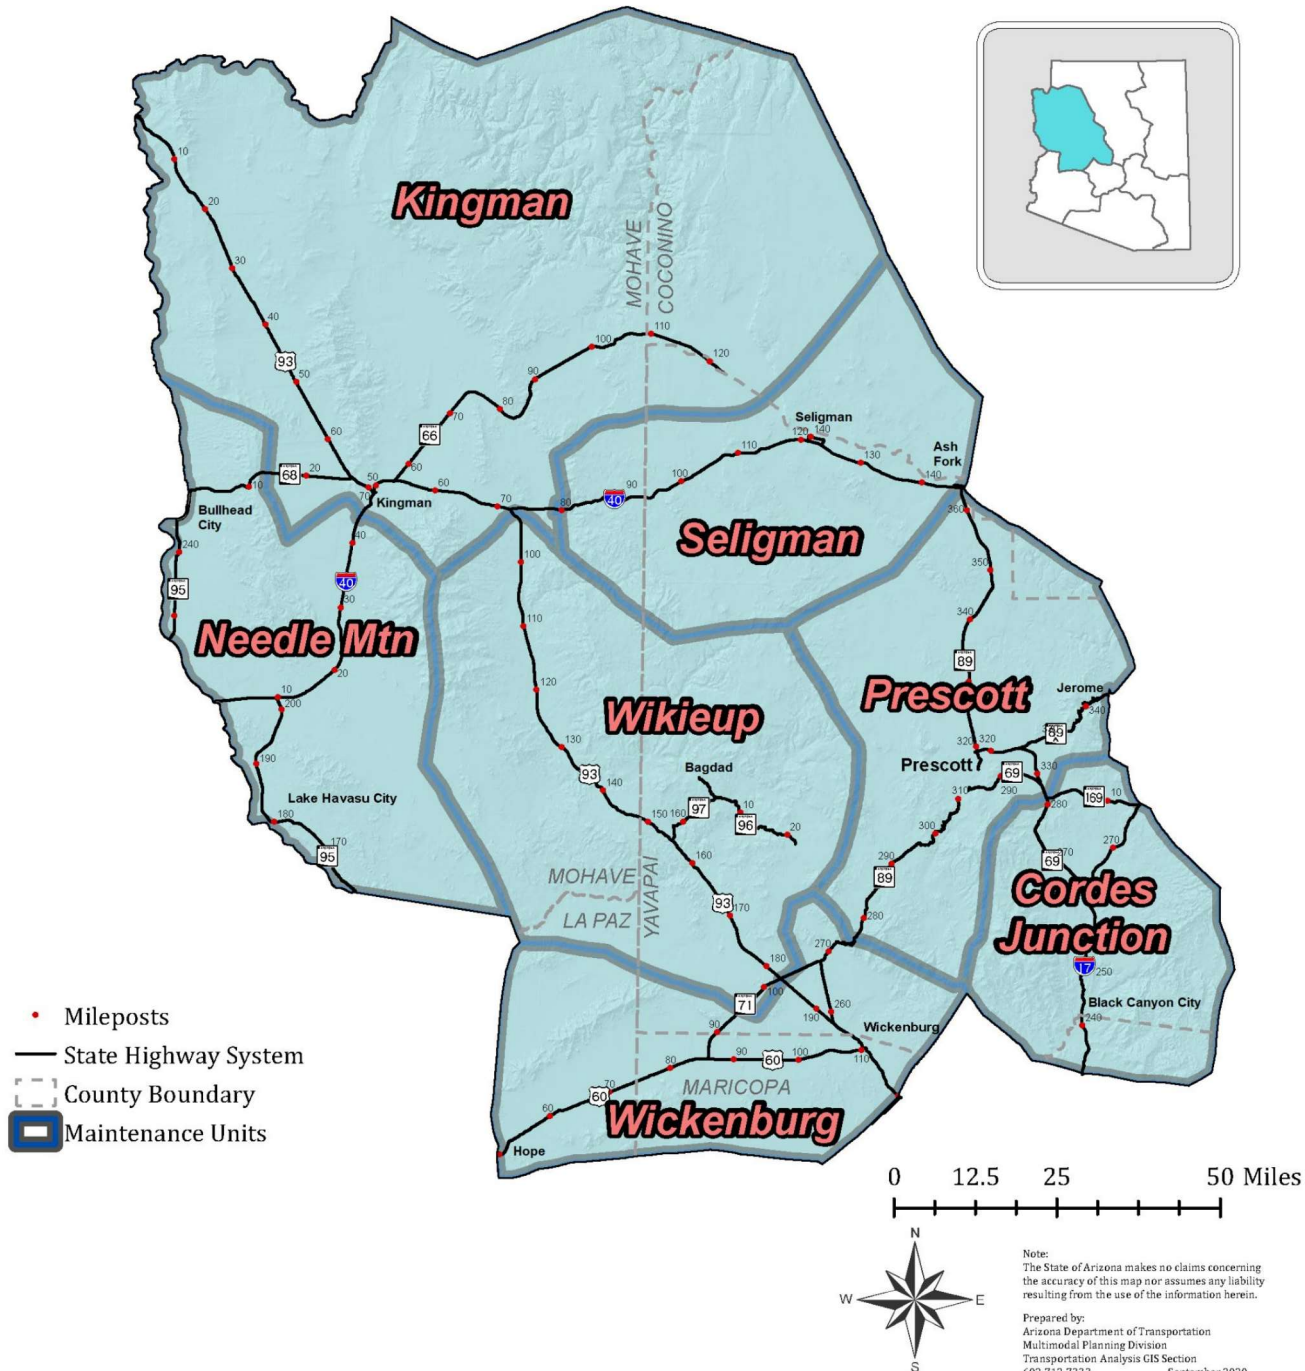

Cordes Junction
15001 S. SR 69
Cordes Junction, AZ 86333
I-17 /SR 69: @ MP 263.0
I-17: MP 232.0 - MP 278.3
SR 69: MP 262.9 - MP 281.1
SR 169: MP 0.0 - MP 15.1

Jonathan Edwards
Supervisor
Unit 5312
928-277-2780

Kingman
3660 East Andy Devine
Kingman, AZ 86401
I-40: MP 44.0 - MP 72.60
US 93: MP 0.0 - MP 71.2
SR 68: MP 0.0 - MP 27.47
Historical Route 66 in City of Kingman
Route 66: MP 56.8 - MP 123.17

Daniel Carlson
Supervisor
Unit 5319
928-681-6012

Needle Mountain
6153 Needle Mountain Rd
Needle Mountain AZ 86436
I-40: MP 0.0 - MP 44.0
SR 95: MP 161.7 - MP 202.0
SR 95: MP 226.2 - MP 250.0

Jeff Baumeister
Supervisor
Unit 5321
928-768-4355

Prescott Valley
6989 E 2nd St.
Prescott Valley, AZ 86314
SR 69: MP 281.06 - MP 296.34
SR 89: MP 276.39 - MP 310.26
SR 89: MP 312.7 - MP 312.9
SR 89: MP 319.01 - MP 347.50
SR 89A: MP 317.42 - MP 349.0
SR 89A Spur: MP 324.47 - MP 331.85

TJ Soto
Supervisor
Unit 5311
928-277-2926

Seligman
I-40 Exit 121 Business Loop 139.8
Seligman AZ 86337
I-40: MP 72.60 - MP 146.23
B-40 (Historical Route 66):
Seligman MP 138.81 - MP 143.04
Ash Fork MP 144.87 - MP 146.37
SR 89: MP 347.50 - 363.80

Raul Martinez
Supervisor
Unit 5320
928-422-3482

Wickenburg
600 B Wickenburg Way
Wickenburg, AZ 85390
US 60 @ MP 111.3
US 60: MP 49.6 - MP 120.1
SR 71: MP 85.8 - MP 109.7
SR 89: MP 258.0 - MP 276.4
US 93: MP 182.9 - MP 199.7

Brent Brinkley
Supervisor
Unit 5313
928-684-3528

Wikieup
17909 S Hwy 93 MP 123.5
Wikieup, AZ 85360
US 93: MP 91.2 - MP 182.9
SR 96: MP 0.0 - MP 22.0
SR 97: MP 155.2 - MP 167.0

Kevin Withrow
Supervisor
Unit 5322
928-530-1184

Roadway Maintenance
6989 E Second St.
Prescott Valley AZ 86314
Northwest District Routes

Dustin Hathaway
Supervisor
Unit 5310
928-277-2938

**PRESCOTT VALLEY CONSTRUCTION
UNIT 4511**

6989 E 2nd St. Prescott Valley, AZ 86314
Senior R.E. : Joshua Wentzlof 928.277.2910
Resident Engineer. : Kara Lavertue 928.277.2913

**SR 89; W Road 5 North-Paulden
(F055901C)**

49% Complete/Bid Amount \$384,444.00
Centerline and Edgeline Rumble Strips
Contractor: Hawk Contracting, LLC
R.E. Kara Lavertue

**SR 89; Little Ranch Road Intersection
(F056501C)**

92% Complete/Bid Amount \$1,141,058.90
Left Turn Lane Construction
Contractor: Asphalt Paving & Supply, Inc.
R.E. Kara Lavertue

**SR 89; Paulden-Old Highway 89
(F063501C)**

0% Complete/Bid Amount \$2,257,592.73
Two Way Left Turn Median
Contractor: Asphalt Paving & Supply, Inc.
R.E. Kara Lavertue

**SR 89AS: Robert Rd-Lynx Creek Bridge
(F069501C)**

93% Complete/Bid Amount \$5,498,106.67
Pavement Life Extension
Contractor: Cactus Transport II, LLC
R.E. Kara Lavertue



**PRESCOTT VALLEY CONSTRUCTION
UNIT 4511**

6989 E 2nd St. Prescott Valley, AZ 86314
Senior R.E. : Joshua Wentzlof 928.277.2910
Resident Engineer. : Kara Lavertue 928.277.2913

**US 60; Centennial Wash Bridge
(F029701C)**

98% Complete/Bid Amount \$13,707,564.30
Bridge Replacement
Contractor: FNF Construction, Inc.
R.E. Chris Page

**SR 69; Prescott Lakes Parkway to Heather
Heights
(H873901C)**

69% Complete/Bid Amount \$9,792,000.00
Roadway Widening
Contractor: FANN Contracting, Inc.
R.E. Kara Lavertue

**SR 69; Lee Blvd to Walker Rd.
(F063301C)**

0% Complete/Bid Amount \$2,261,826.71
Third Lane Extension/Raised Median
Contractor: Sema Construction, Inc.
R.E. Kara Lavertue

**YYV: Williamson Valley R @ Stazenski Road
(T047701C)**

7% Complete/Bid Amount \$479,845.00
Left Turn Lane
Contractor: Earth Resources Corporation
R.R. Kara Lavertue

**Alternate Delivery Project
Public Private Partnership (P3)
Design, Build, Operate, and Maintain (DBOM)**

**I-17; Anthem Way TI to Sunset Point TI
(H680001C)**

D&C Contract Amount \$362,077,500.00
O&M Contract Amount \$2,079,820.00
Widen Roadway/ Flex Lanes
Contractor: Kiewit-Fann Joint Venture
R.E. Josh Wentzlof

**KINGMAN CONSTRUCTION
UNIT 4517**

3660 E Andy Devine Kingman, AZ 86401
Senior R.E.: Darin Dryden 928.681.6046
Resident Engineer: Hien Nguyen 928.681.6030

**US 93; Cane Springs
(F060101C)**

37% Complete/Bid Amount \$48,750,981.10
Roadway Widening
Contractor: FNF Construction, Inc.
R.E. Robert Winrow

**US 93; Kingman POE
(F058901C)**

37% Complete/Bid Amount \$ 2,268,611.73
Install Truck Screening Sensors
Contractor: William Charles Construction Company
R.E. Robert Winrow

**US 93; E. Oldeup Hillside-North of Nothing
(F064901C)**

28% Complete/Bid Amount \$22,414,689.35
Pavement Rehabilitation
Contractor: FNF Construction, Inc.
R.E. Joselyn Valero

**US 93; MP 172-Moore Ranch Rd.
(F059201C)**

0% Complete/Bid Amount \$15,897,676.43
Pavement Preservation
Contractor: FNF Construction, Inc.
R.E. Daniel DeVore

**I-40; E. Kingman TI OP WB Bridge #1358
(F029501C)**

86% Complete/Bid Amount \$8,563,137.57
Bridge Rehabilitation
Contractor: Technology Construction, Inc.
R.E. Darin Dryden

**I-40/US 93; West Kingman TI
(H799301C)**

44% Complete/Bid Amount \$106,543,210.00
Systems to System Interchange
Contractor: Fisher Sand & Gravel Co.
R.E. William Sloan

**KINGMAN CONSTRUCTION
UNIT 4517**

3660 E Andy Devine Kingman, AZ 86401
Senior R.E.: Darin Dryden 928.681.6046
Resident Engineer: Hien Nguyen 928.681.6030

**I-40; Holy Moses Wash-Rattlesnake Wash
(F058501C)**

8% Complete/Bid Amount \$25,252,525.25
Pavement Preservation
Contractor: Fisher Sand & Gravel Co.
R.E. Hien Nguyen

**I-40; CA Border-Needle Mountain Rd.
(F055701C)**

91% Complete/Bid Amount \$8,517,436.81
Pavement Rehabilitation
Contractor: FNF Construction, Inc.
R.E. Joselyn Valero

**I-40; Needle Mountain TI-Lake Havasu TI
(F034201C)**

95% Complete/Bid Amount \$24,777,783.80
Pavement Rehabilitation
Contractor: FNF Construction, Inc.
R.E. Joselyn Valero

**I-40; Rancho Santa Fe Parkway TI
(H681401C)**

31% Complete/Bid Amount \$43,950,204.76
TI Improvements
Contractor: Pulice Construction, Inc.
R.E. Darin Dryden

**I-40; Fort Rock Rd-Markham Wash (WB)
(F073201C)**

0% Complete/Bid Amount \$8,044,142.00
Pavement Life Extension
Contractor: Sunland Asphalt & Construction, LLC
R.E. Daniel DeVore

**MMO: Northern Avenue Complete Streets
(T027201C)**

53% Complete/Bid Amount \$5,848,154.75
Sidewalks, Bike Lanes, Traffic Signal
Contractor: Technology Construction, Inc.
R.E. Hien Nguyen

**KINGMAN CONSTRUCTION
UNIT 4517**

3660 E Andy Devine Kingman, AZ 86401
Senior R.E.: Darin Dryden 928.681.6046
Resident Engineer: Hien Nguyen 928.681.6030

**LHC; McCulloch Blvd. & Jamaica Blvd.
(T039901C)**

9% Complete/Bid Amount \$1,252,101.40
Install Traffic Signal
Contractor: Combs Construction Company, Inc.
R.E. Hien Nguyen

**LHC: S. Palo Verde Blvd-Price Rd
(F064801C)**

0% Complete/Bid Amount \$2,825,500.00
Raised Medians
Contractor: Combs Construction Company, Inc.
R.E. Robert Winrow

**City of Kingman; Andy Devine Ave & Various Loc
(T042101C)**

100% Complete/Bid Amount \$1,061,908.25
Street Improvements
Contractor: Falcone Bros & Associate, Inc.
R.E. Darin Dryden



For Current Road Conditions and
Traffic Alerts:
Dial 5-1-1 (inside AZ)
1.888.411.ROAD (Outside AZ)
Or www.az511.gov on the web

ADVERTISED PROJECTS

**MMO; US 93 to Lloyd Road
(T046101C) Rumble Strips
\$492,591**

**US 60; Morristown-Wickenburg
(F068401C) Pavement Rehabilitation
\$10,400,000**

**US 93; W Tony Ave-N of Bonanza Dr
(F069001C) Striping & Signing
\$2,550,000**

**I-17; Sunset Point to SR 69
(F075801C) Pavement Rehabilitation
\$10,000,000**

**US 93; Sanctuary Rd-I-40 Sacramento Wash
(F055201C) Pavement Preservation
\$78,000,000**

**US 60/US93; Wickenburg ADA Upgrade
(F074101C) Ramps, Sidewalks, Driveways
\$1,000,000**

**LHC; Various Locations
(T043501C) Install Speed Feedback Signs
\$742,500**

**Wash Bridge Walnut Grove Rd/Wagoner Rd
(T041401C) Bridge Replacement
\$951,771**

Future Construction Projects

List not all inclusive

**US 93; Placeritas Creek to Date Creek
(F063801C) Pavement Preservation
\$ 43,552,280 (1st QTR)**

**SR 89; N of Paulden and S of I-40 NB
(F063401C) Northbound Passing Lane
\$1,561,194 (1st QTR)**
