



**PRIORITY PLANNING ADVISORY COMMITTEE  
(PPAC)**

**AGENDA**

**MEETING OF:**

**Wednesday, April 6, 2022**



## ADOT’S NONDISCRIMINATION NOTICE TO THE PUBLIC

The Arizona Department of Transportation (ADOT) hereby gives public notice that it is the Agency’s policy to assure full compliance with Title VI of the Civil Rights Act of 1964, Title II of the Americans with Disabilities Act of 1990 (ADA), and other related authorities in all of its programs and activities.

ADOT’s Title VI and ADA Programs require that no person shall, on the grounds of race, color, national origin, or disability, be excluded from participation in, be denied the benefits of, or be otherwise subjected to discrimination under any program or activity.

Any person, who believes his/her Title VI or ADA rights have been violated, may file a complaint. Any such complaint must be in writing and filed with the ADOT Civil Rights Office within one hundred eighty (180) days following the date of the alleged discriminatory occurrence. For additional information about ADOT’s Civil Rights programs and the procedures to file a complaint contact ADOT Civil Rights Office via the information listed below:

## AVISO PÚBLICO DE LA LEY DE NO-DISCRIMINACIÓN DE ADOT

El Departamento de Transporte del Estado de Arizona (ADOT) informa al público que esta agencia tiene como regla asegurar el cumplimiento total del Título VI de la Ley de los Derechos Civiles de 1964, del Título II de la Ley de ciudadanos Americanos con Discapacidades de 1990 (ADA) y otras normas relacionadas con todos sus programas y actividades.

Los programas del Título VI y ADA de ADOT exigen que a ninguna persona se le excluya de participar, se le nieguen beneficios o de ninguna otra manera sea sujeta a discriminación en ningún programa o actividad de ADOT por motivo de raza, color, país de origen, o discapacidad.

Cualquier persona que crea que se han violado sus derechos bajo el Título VI o el ADA, puede presentar una queja. Esta queja debe presentarse por escrito a la Oficina de Derechos Civiles de ADOT dentro de ciento ochenta (180) días a partir de la fecha en que se alega que ocurrió la discriminación. Para recibir más información sobre los programas de Derechos Civiles de ADOT y los procedimientos para presentar una queja, por favor póngase en contacto con la Oficina de Derechos Civiles de ADOT a través la información que aparece abajo:

**FELICIA BELTRAN**  
TITLE VI NONDISCRIMINATION  
PROGRAM COORDINATOR  
[FBELTRAN@AZDOT.GOV](mailto:FBELTRAN@AZDOT.GOV)  
**KRYSTAL SMITH**  
ADA/NONDISCRIMINATION  
PROGRAM COORDINATOR  
[KSMITH2@AZDOT.GOV](mailto:KSMITH2@AZDOT.GOV)

**ADOT Civil Rights Office**  
206 S. 17th Avenue, Mail Drop 155-A  
Phoenix, AZ 85007  
602.712.8946  
602.239.6257 FAX  
[azdot.gov](http://azdot.gov)

**ARIZONA DEPARTMENT OF TRANSPORTATION  
MULTIMODAL PLANNING DIVISION  
OFFICE MEMO**

TO: PRIORITY PLANNING ADVISORY COMMITTEE MEMBERS

KRISTINE WARD  
STEVE BOSCHEN  
BRENT CAIN  
CLEMENC LIGOCKI  
TIM LANE  
BARRY CROCKETT  
DON KRIZ  
JON BRODSKY (NON-VOTING)

FROM: Chariman Paul Patane

SUBJECT: PRIORITY PLANNING ADVISORY COMMITTEE MEETING (PPAC)

Pursuant to the A.R.S. 28-6951(B), the ADOT Director has appointed the members of the Priority Planning Advisory Committee (PPAC) to develop the Five Year Transportation Facilities Construction Program. This meeting is scheduled, pursuant to 28-6951(C4), to review the Program and make changes and schedule new projects into the adopted Five Year Transportation Facilities Construction Program.

Pursuant to Title VI of the Civil Rights Act of 1964, and the Americans with Disabilities Act (ADA), ADOT does not discriminate on the basis of race, color, national origin, age, sex or disability. Persons who require a reasonable accommodation based on language or disability should contact ADOT's Civil Rights Office at 602.712.8946 or at [civilrightsoffice@azdot.gov](mailto:civilrightsoffice@azdot.gov). Requests should be made as early as possible to ensure the State has an opportunity to address the accommodation.

The meeting of the Arizona Department of Transportation, Priority Planning Advisory Committee (PPAC) will be held on Wednesday April 6, 2022 at 9:00AM. This will be a teleconference meeting. To access the meeting through Internet, please go to [meet.google.com/vxe-iwaq-adb](https://meet.google.com/vxe-iwaq-adb). To access the meeting by phone, please dial +1 904-580-9875 PIN: 480 616 971#.


**AGENDA:**

1. Call to Order	Chairman
2. Roll Call	Information Only
3. Title VI the Civil Rights Act of 1964, as Amended	Information Only
4. Call to Audience	Information Only
5. Approval of the Meeting Minutes on 3/2/2022	Discussion and Possible Action
6. Program Monitoring Report	Information & Discussion

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-1	<b>Route &amp; MP:</b>	Local
	<b>Project Name:</b>	PHASE III-CITY OF GLENDALE FLASHING YELLOW ARROWS
	<b>Type of Work:</b>	CONVERSION TO FLASHING YELLOW ARROWS
	<b>County:</b>	Maricopa
	<b>District:</b>	Central
	<b>Schedule:</b>	
	<b>Project:</b>	T011901C TIP#: 102068
	<b>Project Manager:</b>	Angela Galietti
	<b>Program Amount:</b>	\$0
	<b>New Program Amount:</b>	\$2,758,000
	<b>Requested Action:</b>	Establish construction project.

---

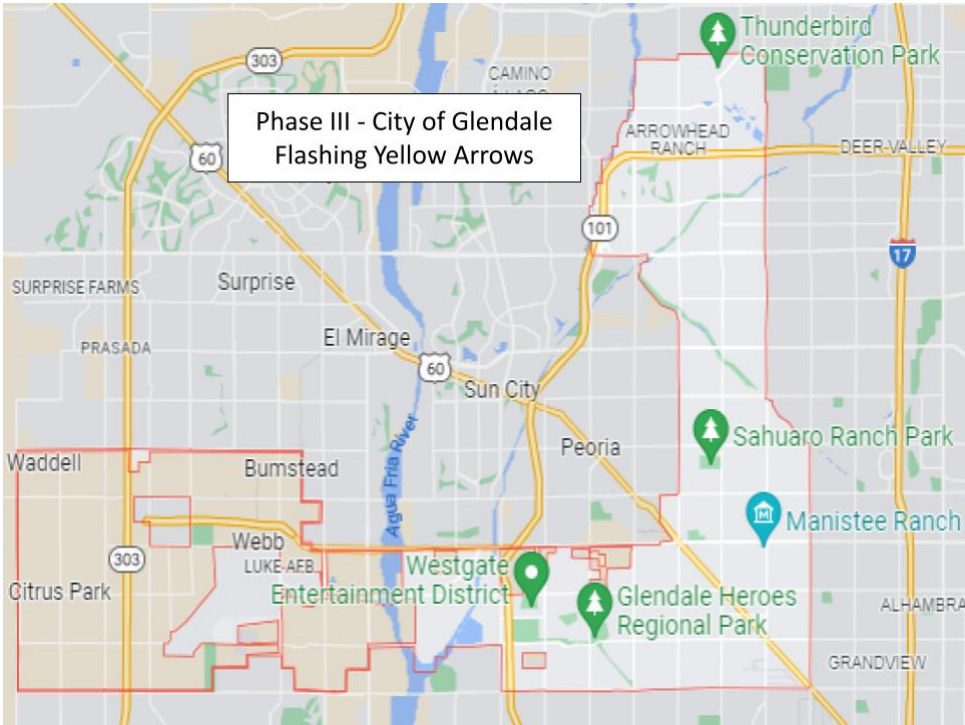

01

1. PRB Meeting Date: 3/22/2022

2. Teleconference: No

3. Form Date / 5. Form By:

4. Project Manager / Presenter:

3/24/2022

Angela Galietti @

Angela Galietti

205 S 17th Ave - 4983 PROJECT MANAGEMENT

6. Project Name:

7. Type of Work:

PHASE III-CITY OF GLENDALE FLASHING YELLOW ARROWS

CONVERSION TO FLASHING YELLOW ARROWS

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
<a href="#">GD10</a>	Central	0000	Maricopa	GLN	T011901C	0.0	HSIPGLN-0(259)T

16. Program Budget: \$0

17. Program Item #: 102068

18. Current Approved Program Budget:

18a. (+/-) Program Budget Request:

18b Total Program Budget After Request:

\$0

\$2,758

\$2,758

**CURRENTLY APPROVED:****19. BUDGET ITEMS:****CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
70122	\$2,255	MODERNIZATION	100pct HSIP for signals
70122	\$474	MODERNIZATION	94.3pct HSIP for geometric and retroreflective upgrades
OTHR22	\$29	.	City of Glendale 5.7pct match.

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUESTNEW SCHEDULE:**

21A. REQUEST FISCAL YEAR: 22

22A. REQUEST BID READY:

23A. REQUEST ADV DATE: 4/13/2022

20. JPA #'s: 21-0008196-I SIGNED: YES ADV: YES

<b>CHANGE IN:</b>	24a. PROJECT NAME:	NO	24b. TYPE OF WORK:	NO	24c. SCOPE:	NO	24d. CURRENT STAGE:	STAGE V
-------------------	--------------------	----	--------------------	----	-------------	----	---------------------	---------

24e. ENVIRONMENTAL CLEARANCE: YES

24f. MATERIALS MEMO COMP: NOT APPLICABLE

24g. U&amp;RR CLEARANCE: YES

24h. C&amp;S CLEARANCE: NO

24i. R/W CLEARANCE: YES

24j. CUSTOMIZED SCHEDULE: NO

24k. SCOPING DOCUMENT: NOT APPLICABLE

**25. DESCRIPTION OF REQUEST**

Establish construction project.

**26. JUSTIFICATION OF REQUEST**

This request is to establish a construction project installing safety improvements for the Phase III flashing yellow arrows and median modifications for the City of Glendale. This is a local project with the City of Glendale. HSIP covers 100pct of the traffic signal upgrades and HSIP covers 94.3pct of the geometric changes and retroreflective upgrades.

MAG TIP ID: GLN22-801

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

ESTABLISH A NEW PROJECT

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 4/6/2022

**PRB APPROVED**



7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-2	Route & MP:	SR 287 @ MP 116.7
	Project Name:	HACIENDA - SR 87
	Type of Work:	RUMBLE STRIPS AND RIGHT TURN LANE
	County:	Pinal
	District:	Southcentral
	Schedule:	FY 2022
	Project:	F035701C TIP#: 101007
	Project Manager:	Dave Sabers
	Program Amount:	\$530,000
	New Program Amount:	\$740,000
	Requested Action:	Increase budget.

---



04

1. PRB Meeting Date: 3/22/2022

2. Teleconference: No

3. Form Date / 5. Form By:

3/24/2022

Dave Sabers

4. Project Manager / Presenter:

Dave Sabers @ (602) 712-7345

205 S 17 Ave - 4983 PROJECT MANAGEMENT

6. Project Name:

HACIENDA - SR 87

7. Type of Work:

RUMBLE STRIPS AND RIGHT TURN LANE

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
CO1P	Southcentral	287	Pinal	116.7	F035701C ?	9.22	HSIP287-A(202)T

16. Program Budget: \$530

17. Program Item #: 101007

18. Current Approved Program Budget:

\$530

18a. (+/-) Program Budget Request:

\$210

18b Total Program Budget After Request:

\$740

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
101007	\$530	Hacienda to SR-87	.

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR: 22  
 22. CURRENT BID READY: 4/22/2022  
 23. CURRENT ADV DATE: 5/6/2022

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
70122	\$210	MODERNIZATION	

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:  
 22A. REQUEST BID READY:  
 23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED:

NO

ADV: NO



PROJECT FUNDING VERIFIED BY PM

**CHANGE IN:** 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: STAGE V

24e. ENVIRONMENTAL CLEARANCE: YES

24g. U&amp;RR CLEARANCE: YES

24i. R/W CLEARANCE: YES

24k. SCOPING DOCUMENT: YES

24f. MATERIALS MEMO COMP: YES

24h. C&amp;S CLEARANCE: YES

24j. CUSTOMIZED SCHEDULE: YES

**25. DESCRIPTION OF REQUEST**

Increase budget.

**26. JUSTIFICATION OF REQUEST**

This is a HSIP Project. Project is at post Stage IV submittal, all comment responses have been accepted and the team is finalizing the project documents. The additional cost includes adding fog coat to the rumble strip areas to protect the pavement (5K), additional traffic control and pavement marking resulting from the fog coat (80K), increases in quantities as the design was advanced (traffic items for the right turn lane increased 25K, roadway items for the right turn lane increased 7K), and unit price increases. Construction engineering for the District increased 15K. The construction cost is based on the C&S budget recap. Due to these items, the project is estimated to require additional construction funding. Construction contingency (5 pct) and ICAP increased based on the other increases. ICAP is included in this request.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**


REQUEST APPROVED  
 SUBJECT TO PPAC APPROVAL - 4/6/2022

**PRB APPROVED**

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-3	<b>Route &amp; MP:</b>	I-10 @ MP 240
	<b>Project Name:</b>	TANGERINE RD - ALVERNON WAY
	<b>Type of Work:</b>	Upgrade Traffic Signal Equipment
	<b>County:</b>	Pima
	<b>District:</b>	Southcentral
	<b>Schedule:</b>	
	<b>Project:</b>	F049201X TIP#: 102991
	<b>Project Manager:</b>	James Gomes
	<b>Program Amount:</b>	\$0
	<b>New Program Amount:</b>	\$112,000
	<b>Requested Action:</b>	Establish new project.

---

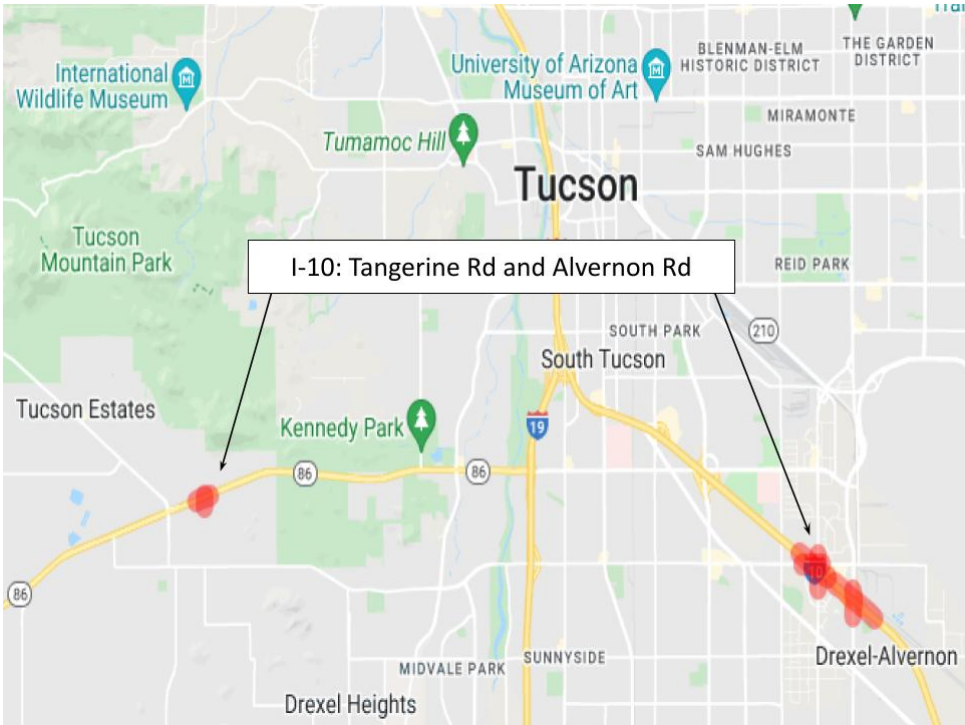



09

1. PRB Meeting Date: 3/8/2022



2. Teleconference: (520) 388-4231

3. Form Date / 5. Form By:

3/10/2022

James Gomes

4. Project Manager / Presenter:

James Gomes @ (520) 388-4231

1221 S 2nd Ave, , T100 - 6500 OPERATIONAL TRAFFIC &amp; SAFETY ADMINISTRAT

6. Project Name:

TANGERINE RD - ALVERNON WAY

7. Type of Work:

Upgrade Traffic Signal Equipment

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
VW1P	Southcentral	10	Pima	240	F049201X ?	24	010-D(225)T

16. Program Budget: \$0

17. Program Item #: 102991

18. Current Approved Program Budget:

\$0

18a. (+/-) Program Budget Request:

\$112

18b Total Program Budget After Request:

\$112

**CURRENTLY APPROVED:****19. BUDGET ITEMS:****CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
80607	\$112	.	PAG RTA STBGP funds

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUESTNEW SCHEDULE:**

21A. REQUEST FISCAL YEAR: 22

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED:

NO

ADV:

NO



PROJECT FUNDING VERIFIED BY PM

<b>CHANGE IN:</b>	24a. PROJECT NAME:	NO	24b. TYPE OF WORK:	NO	24c. SCOPE:	NO	24d. CURRENT STAGE:	NOT APPLICABLE
-------------------	--------------------	----	--------------------	----	-------------	----	---------------------	----------------

24e. ENVIRONMENTAL CLEARANCE: NOT APPLICABLE

24g. U&amp;RR CLEARANCE: NOT APPLICABLE

24i. R/W CLEARANCE: NOT APPLICABLE

24k. SCOPING DOCUMENT: NOT APPLICABLE

24f. MATERIALS MEMO COMP: NOT APPLICABLE

24h. C&amp;S CLEARANCE: NOT APPLICABLE

24j. CUSTOMIZED SCHEDULE: NOT APPLICABLE

**25. DESCRIPTION OF REQUEST**

Establish new project

**26. JUSTIFICATION OF REQUEST**

The South Central Traffic Operations (Unit 6543) requests to upgrade 5 TS-1 traffic signal cabinets with TS-2, Type 1 cabinets and controllers along I-10 within Pima County. This Project will utilize PAG RTA STBGP funds TIP ID 3.22 to purchase traffic signal equipment to upgrade to current standards. There is a 100pct federal contribution, no local match needed.

The Project locations include I-10 at Tangerine, at Irvington, at Palo Verde, at Alvernon, and SR 86 at Camino De Oeste.

The Project will utilize ADOT manpower to remove the existing traffic signal cabinets and replace with the new TS-2, Type 1 cabinets and controller at the 5 locations.

This is a Procurement project.

ICAP is included in the project estimate.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

ESTABLISH A NEW PROJECT

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED

SUBJECT TO PPAC APPROVAL - 4/6/2022

**PRB APPROVED**

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-4	<b>Route &amp; MP:</b>	Various Routes
	<b>Project Name:</b>	SR 87, SR 179 & SR-260
	<b>Type of Work:</b>	TREE REMOVAL
	<b>County:</b>	Coconino
	<b>District:</b>	Northcentral
	<b>Schedule:</b>	FY 2022
	<b>Project:</b>	F042101C TIP#: 101009
	<b>Project Manager:</b>	Judah Cain
	<b>Program Amount:</b>	\$1,549,000
	<b>New Program Amount:</b>	\$2,620,000
	<b>Requested Action:</b>	Defer Project to FY23. Increase Budget.

---



08

1. PRB Meeting Date: 3/8/2022

2. Teleconference: No

3. Form Date / 5. Form By:

3/10/2022

Judah Cain

4. Project Manager / Presenter:

Judah Cain @

,, - 4983 PROJECT MANAGEMENT

6. Project Name:

SR 87, SR 179 &amp; SR-260

7. Type of Work:

TREE REMOVAL

8. CPSID:

CP1P

9. District:

Northcentral

10. Route:

999

11. County:

Coconino

12. Beg MP:

0.0

13. TRACS #:

F042101C ?

14. Len (Mi.):

54.3

15. Fed Id #:

HSIP 999-A(554)T

16. Program Budget: \$1,549

17. Program Item #: 101009

18. Current Approved Program Budget:

\$1,549

18a. (+/-) Program Budget Request:

\$1,071

18b Total Program Budget After Request:

\$2,620

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
70122	\$1,549	MODERNIZATION	.

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
70123	\$2,620	MODERNIZATION	.
70122	(\$1,549)	MODERNIZATION	.

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR: 22

22. CURRENT BID READY:

23. CURRENT ADV DATE: 6/30/2022

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR: 23

22A. REQUEST BID READY: TBD

23A. REQUEST ADV DATE: TBD

20. JPA #'s:

SIGNED: NO

ADV: NO

**CHANGE IN:** 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: NOT APPLICABLE

24e. ENVIRONMENTAL CLEARANCE: NO

24f. MATERIALS MEMO COMP: NO

24g. U&amp;RR CLEARANCE: NO

24h. C&amp;S CLEARANCE: NO

24i. R/W CLEARANCE: NO

24j. CUSTOMIZED SCHEDULE: NO

24k. SCOPING DOCUMENT: NO

**25. DESCRIPTION OF REQUEST**

Defer Project to FY23.

Increase Budget.

**26. JUSTIFICATION OF REQUEST**

This tree removal project requires a cultural survey that is scheduled to begin in May 2022 with anticipated completion in August 2022. Based on this timeline the project team recommends advertising this project in the second quarter of Fiscal Year (FY23).

The project construction costs were reviewed by the consultant designer and revisions to the estimate were made based on meetings to discuss lessons learned with the respective Districts following the construction of two tree removal projects in FY22.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN SCHEDULE  
CHANGE IN FY  
CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 4/6/2022

**PRB APPROVED**

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-5	Route & MP:	I-17 @ MP 203.0
	Project Name:	INDIAN SCHOOL RD TI
	Type of Work:	CONSTRUCT TI
	County:	Maricopa
	District:	Central
	Schedule:	FY 2022
	Project:	F016601C TIP#: 8888
	Project Manager:	Trent Kelso
	Program Amount:	\$46,611,000
	New Program Amount:	\$48,392,000
	Requested Action:	Defer Project to FY 23.

---



01

1. PRB Meeting Date: 3/15/2022

2. Teleconference: No

3. Form Date / 5. Form By:

3/17/2022

Trent Kelso

4. Project Manager / Presenter:

Trent Kelso @ (602) 712-6685

205 S 17th Ave, 295., 614E - 4980 ENGINEERING CONSULTANT SECT

6. Project Name:

INDIAN SCHOOL RD TI

7. Type of Work:

CONSTRUCT TI

8. CPSID:

MD10

9. District:

Central

10. Route:

17

11. County:

Maricopa

12. Beg MP:

203.0

13. TRACS #:

F016601C ?

14. Len (Mi.):

0.5

15. Fed Id #:

NHPP017-A(BFN)T

16. Program Budget: \$46,611

17. Program Item #: 8888

18. Current Approved Program Budget:

\$46,611

18a. (+/-) Program Budget Request:

\$1,781

18b Total Program Budget After Request:

\$48,392

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
8888	\$35,421	INDIAN SCHOOL RD TI	ISR NHPP funding 35,420,801
8888	\$11,190	INDIAN SCHOOL RD TI	RARF Match 11,190,067

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
49822	(\$35,421)	.	NHPP 35,420,801
49922	(\$11,190)	.	RARF FUNDS 11,190,067
49823	\$36,774	.	NHPP FUNDS - \$36,773,876
49923	\$11,618	.	RARF FUNDS - \$11,617,527

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR: 22

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST/NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR: 23

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s: SIGNED: NO ADV: NO

CHANGE IN: 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: STAGE I

24e. ENVIRONMENTAL CLEARANCE: YES

24f. MATERIALS MEMO COMP: NO

24g. U&amp;RR CLEARANCE: NO

24h. C&amp;S CLEARANCE: NO

24i. R/W CLEARANCE: NO

24j. CUSTOMIZED SCHEDULE: NO

24k. SCOPING DOCUMENT: NO

**25. DESCRIPTION OF REQUEST**

Defer Project to FY23

**26. JUSTIFICATION OF REQUEST**

Due to changing priorities in the MAG region, this project was deferred to FY 2023 by MAG at the 1/26 Regional Council Meeting and approved on 2/4/2022.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**CHANGE IN FY  
CHANGE IN BUDGET**APPROVED / RECOMMENDED ACTIONS:**REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 4/6/2022**PRB APPROVED**



7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-6	<b>Route &amp; MP:</b>	Local
	<b>Project Name:</b>	CORNVILLE RD, TISSAW - BEAVERHEAD FLAT RD
	<b>Type of Work:</b>	INSTALL RUMBLE STRIPS & WIDEN SHOULDERS
	<b>County:</b>	Yavapai
	<b>District:</b>	Northcentral
	<b>Schedule:</b>	
	<b>Project:</b>	T028401C TIP#: 101776
	<b>Project Manager:</b>	Trent Kelso
	<b>Program Amount:</b>	\$0
	<b>New Program Amount:</b>	\$3,468,000
	<b>Requested Action:</b>	Establish New Project.

---



05

1. PRB Meeting Date: 3/15/2022

2. Teleconference: No

3. Form Date / 5. Form By:

3/17/2022

Trent Kelso

4. Project Manager / Presenter:

Trent Kelso @ (602) 723-8313

205 S 17th Ave, 295., 614E - 4980 ENGINEERING CONSULTANT SECT

6. Project Name:

CORNVILLE RD, TISSAW - BEAVERHEAD FLAT RD

7. Type of Work:

INSTALL RUMBLE STRIPS &amp; WIDEN SHOULDERS

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
OB1P	Northcentral	0000	Yavapai	YYV	T028401C ?	5.0	HSIPYYV-0(210)T

16. Program Budget: \$0

17. Program Item #: 101776

18. Current Approved Program Budget:

\$0

18a. (+/-) Program Budget Request:

\$3,468

18b Total Program Budget After Request:

\$3,468

**CURRENTLY APPROVED:****19. BUDGET ITEMS:****CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
70123	\$3,270	MODERNIZATION	.
OTHR23	\$198	.	Yavapai County Local Match

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST/NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

23

22A. REQUEST BID READY:

8/15/2022

23A. REQUEST ADV DATE:

9/15/2022

20. JPA #'s: IGA 20-0008006-I SIGNED: YES ADV: YES

CHANGE IN: 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: STAGE II

24e. ENVIRONMENTAL CLEARANCE: NO

24f. MATERIALS MEMO COMP: NO

24g. U&amp;RR CLEARANCE: NO

24h. C&amp;S CLEARANCE: NO

24i. R/W CLEARANCE: NO

24j. CUSTOMIZED SCHEDULE: YES

24k. SCOPING DOCUMENT: NO

**25. DESCRIPTION OF REQUEST**

Establish new Project

**26. JUSTIFICATION OF REQUEST**

The project contains a new easement from Coconino National Forest, which will take a minimum of two months to obtain after environmental approval. With the environmental clearance scheduled for early this summer, the project will be delivered in the first quarter of FY23.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

ESTABLISH A NEW PROJECT

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 4/6/2022

**PRB APPROVED**

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-7	<b>Route &amp; MP:</b>	I-40 @ MP 286.0
	<b>Project Name:</b>	8TH AVE OP EB/WB
	<b>Type of Work:</b>	BRIDGE REHABILITATION
	<b>County:</b>	Navajo
	<b>District:</b>	Northeast
	<b>Schedule:</b>	
	<b>Project:</b>	F042301D TIP#: 100198
	<b>Project Manager:</b>	Tricia Brown
	<b>Program Amount:</b>	\$1,010,000
	<b>New Program Amount:</b>	\$410,000
	<b>Requested Action:</b>	Change budget.

---



01

1. PRB Meeting Date: 3/1/2022



2. Teleconference: (602) 712-7046

3. Form Date / 5. Form By:

3/3/2022

Tricia Brown

4. Project Manager / Presenter:

Tricia Brown @ (602) 712-7046

205 S 17th Ave, , 614E - 4980 ENGINEERING CONSULTANT SECT

6. Project Name:

8TH AVE OP EB/WB

7. Type of Work:

BRIDGE REHABILITATION

8. CPSID:

SX10

9. District:

Northeast

10. Route:

40

11. County:

Navajo

12. Beg MP:

286.0

13. TRACS #:

F042301D

14. Len (Mi.):

1.0

15. Fed Id #:

NHPP

16. Program Budget: \$1,010

17. Program Item #: 100198

18. Current Approved Program Budget:

\$1,010

18a. (+/-) Program Budget Request:

(\$600)

18b Total Program Budget After Request:

\$410

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
100198	\$600		FY22 8th Ave OP EB/WB - Bridge Rehabilitation
100198	\$410		FY21 8th Ave OP EB/WB - Bridge Rehabilitation

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
72322	(\$600)	CONTINGENCY	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED:

NO

ADV: NO



PROJECT FUNDING VERIFIED BY PM

CHANGE IN: 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: NOT APPLICABLE

24e. ENVIRONMENTAL CLEARANCE:

NO

24f. MATERIALS MEMO COMP:

NO

24g. U&amp;RR CLEARANCE:

NO

24h. C&amp;S CLEARANCE:

NO

24i. R/W CLEARANCE:

NO

24j. CUSTOMIZED SCHEDULE:

NO

24k. SCOPING DOCUMENT:

NO

**25. DESCRIPTION OF REQUEST**

Change budget.

**26. JUSTIFICATION OF REQUEST**

This project was inadvertently listed in the 2022-2026 Five-Year Program with \$600K for Design in FY22. Action was taken on April 27, 2021 to establish the design project in FY21. No additional funds are needed in FY22.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 4/6/2022

**PRB APPROVED**

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-8	Route & MP:	I-40 @ MP 318.8
	Project Name:	PINTA - MCCARRELL
	Type of Work:	PAVEMENT REHABILITATION
	County:	Apache
	District:	Southeast
	Schedule:	
	Project:	F049801D TIP#: 102472
	Project Manager:	Tricia Brown
	Program Amount:	\$1,218,000
	New Program Amount:	\$563,000
	Requested Action:	Establish new project.

---





04

1. PRB Meeting Date: 3/1/2022



2. Teleconference: (602) 712-7046

3. Form Date / 5. Form By:

3/3/2022

Tricia Brown

4. Project Manager / Presenter:

Tricia Brown @ (602) 712-7046

205 S 17th Ave, , 614E - 4980 ENGINEERING CONSULTANT SECT

6. Project Name:

PINTA - MCCARRELL

7. Type of Work:

PAVEMENT REHABILITATION

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
SE1P	Southeast	40	Apache	318.8	F049801D ?	11.8	040-E(227)T

16. Program Budget: \$1,218

17. Program Item #: 102472

18. Current Approved Program Budget:

\$1,218

18a. (+/-) Program Budget Request:

(\$655)

18b Total Program Budget After Request:

\$563

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
102472	\$1,218	.	.

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
72322	(\$655)	CONTINGENCY	

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED:

NO

ADV:

NO



PROJECT FUNDING VERIFIED BY PM

<b>CHANGE IN:</b>	24a. PROJECT NAME:	NO	24b. TYPE OF WORK:	NO	24c. SCOPE:	NO	24d. CURRENT STAGE:	NOT APPLICABLE
-------------------	--------------------	----	--------------------	----	-------------	----	---------------------	----------------

24e. ENVIRONMENTAL CLEARANCE:

NO

24f. MATERIALS MEMO COMP:

NO

24g. U&amp;RR CLEARANCE:

NO

24h. C&amp;S CLEARANCE:

NO

24i. R/W CLEARANCE:

NO

24j. CUSTOMIZED SCHEDULE:

NO

24k. SCOPING DOCUMENT:

NO

**25. DESCRIPTION OF REQUEST**

Establish new project.

**26. JUSTIFICATION OF REQUEST**

Pre-scoping has been completed and pavement rehabilitation with minor drainage improvements, slope rehabilitation, and guardrail replacement are recommended. The project is programmed for construction in FY 24.

Staff: \$330k

Consultant: \$179k

ICAP: \$54k

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

ESTABLISH A NEW PROJECT

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED

SUBJECT TO PPAC APPROVAL - 4/6/2022

**PRB APPROVED**

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-9	<b>Route &amp; MP:</b>	SR 80 @ MP 338.6
	<b>Project Name:</b>	MULE PASS TUNNEL, BISBEE
	<b>Type of Work:</b>	SAFETY IMPROVEMENTS
	<b>County:</b>	Cochise
	<b>District:</b>	Southeast
	<b>Schedule:</b>	
	<b>Project:</b>	F039401D TIP#: 102449
	<b>Project Manager:</b>	Tricia Brown
	<b>Program Amount:</b>	\$924,000
	<b>New Program Amount:</b>	\$462,000
	<b>Requested Action:</b>	Change budget.

---



05

1. PRB Meeting Date: 3/22/2022 ☒ 2. Teleconference: (602) 712-7046

3. Form Date / 5. Form By:

3/24/2022

Tricia Brown

4. Project Manager / Presenter:

Tricia Brown @ (602) 712-7046

205 S 17th Ave, , 614E - 4980 ENGINEERING CONSULTANT SECT

6. Project Name:

MULE PASS TUNNEL, BISBEE

7. Type of Work:

SAFETY IMPROVEMENTS

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
RF1P	Southeast	80	Cochise	338.6	F039401D	1.2	HSIP080-A(219)T

16. Program Budget: \$924

17. Program Item #: 102449

18. Current Approved Program Budget:

\$924

18a. (+/-) Program Budget Request:

(\$462)

18b Total Program Budget After Request:

\$462

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
70121	\$462	MODERNIZATION	
102449	\$462	.	FY22 5-Year Program

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
70122	(\$462)	MODERNIZATION	.

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s: SIGNED: NO ADV: NO



PROJECT FUNDING VERIFIED BY PM

CHANGE IN: 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: NOT APPLICABLE

24e. ENVIRONMENTAL CLEARANCE: NO

24f. MATERIALS MEMO COMP: NO

24g. U&amp;RR CLEARANCE: NO

24h. C&amp;S CLEARANCE: NO

24i. R/W CLEARANCE: NO

24j. CUSTOMIZED SCHEDULE: NO

24k. SCOPING DOCUMENT: NO

**25. DESCRIPTION OF REQUEST**

Change budget.

**26. JUSTIFICATION OF REQUEST**

This project was inadvertently listed in the 2022-2026 Five-Year Program with \$462K for Design in FY22. Action was taken on May 4, 2021 to establish the design project in FY21. No additional design funds are needed in FY22.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 4/6/2022

**PRB APPROVED**

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-10	<b>Route &amp; MP:</b>	SR 80 @ MP 338.6
	<b>Project Name:</b>	MULE PASS TUNNEL, BISBEE
	<b>Type of Work:</b>	SAFETY IMPROVEMENTS
	<b>County:</b>	Cochise
	<b>District:</b>	Southeast
	<b>Schedule:</b>	FY 2022
	<b>Project:</b>	F039401C TIP#: 102449
	<b>Project Manager:</b>	Tricia Brown
	<b>Program Amount:</b>	\$3,000,000
	<b>New Program Amount:</b>	\$5,700,000
	<b>Requested Action:</b>	Increase budget.

---



06

1. PRB Meeting Date: 3/22/2022 ☒ 2. Teleconference: (602) 712-7046

3. Form Date / 5. Form By:

3/24/2022

Tricia Brown

4. Project Manager / Presenter:

Tricia Brown @ (602) 712-7046

205 S 17th Ave, , 614E - 4980 ENGINEERING CONSULTANT SECT

6. Project Name:

MULE PASS TUNNEL, BISBEE

7. Type of Work:

SAFETY IMPROVEMENTS

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
RF1P	Southeast	80	Cochise	338.6	F039401C ?	1.2	HSIP080-A(219)T

16. Program Budget: \$3,000

17. Program Item #: 102449

18. Current Approved Program Budget:

\$3,000

18a. (+/-) Program Budget Request:

\$2,700

18b Total Program Budget After Request:

\$5,700

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
102449	\$3,000	.	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR: 22

22. CURRENT BID READY:

23. CURRENT ADV DATE: 6/17/2022

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
70122	\$2,700	MODERNIZATION	HSIP subprogram

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s: SIGNED: NO ADV: NO

☒ PROJECT FUNDING VERIFIED BY PM

CHANGE IN: 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: STAGE IV

24e. ENVIRONMENTAL CLEARANCE: YES

24g. U&amp;RR CLEARANCE: NO

24i. R/W CLEARANCE: YES

24k. SCOPING DOCUMENT: YES

24f. MATERIALS MEMO COMP: NO

24h. C&amp;S CLEARANCE: YES

24j. CUSTOMIZED SCHEDULE: YES

**25. DESCRIPTION OF REQUEST**

Increase budget.

**26. JUSTIFICATION OF REQUEST**

Additional construction funds are needed for increased costs for luminaire items and tunnel work (washing, lighting structure, structure anchors, and water seal) as well as mobilization. A revised HSIP eligibility letter has been issued.

ICAP is included in this request.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 4/6/2022**PRB APPROVED**



7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-11	<b>Route &amp; MP:</b>	I-10 @ MP 90.0
	<b>Project Name:</b>	443RD AVE - E OF WINTERSBURG RD
	<b>Type of Work:</b>	PAVEMENT REHABILITATION
	<b>County:</b>	Maricopa
	<b>District:</b>	Southwest
	<b>Schedule:</b>	FY 2023
	<b>Project:</b>	F034501C TIP#: 101684
	<b>Project Manager:</b>	Tricia Brown
	<b>Program Amount:</b>	\$23,000,000
	<b>New Program Amount:</b>	\$27,000,000
	<b>Requested Action:</b>	Increase budget.

---



07

1. PRB Meeting Date: 3/22/2022 ☒ 2. Teleconference: (602) 712-7046

3. Form Date / 5. Form By:

3/24/2022

Tricia Brown

4. Project Manager / Presenter:

Tricia Brown @ (602) 712-7046

205 S 17th Ave, , 614E - 4980 ENGINEERING CONSULTANT SECT

6. Project Name:

443RD AVE - E OF WINTERSBURG RD

7. Type of Work:

PAVEMENT REHABILITATION

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
MH1P	Southwest	10	Maricopa	90.0	F034501C ?	10.0	010-A(235)T

16. Program Budget: \$23,000

17. Program Item #: 101684

18. Current Approved Program Budget:

\$23,000

18a. (+/-) Program Budget Request:

\$4,000

18b Total Program Budget After Request:

\$27,000

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
72523	\$23,000	PRESERVATION	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR: 23

22. CURRENT BID READY:

23. CURRENT ADV DATE: 8/19/2022

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
72523	\$4,000	PRESERVATION	.

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED:

NO

ADV: NO



PROJECT FUNDING VERIFIED BY PM

<b>CHANGE IN:</b>	24a. PROJECT NAME:	NO	24b. TYPE OF WORK:	NO	24c. SCOPE:	NO	24d. CURRENT STAGE:	STAGE V
-------------------	--------------------	----	--------------------	----	-------------	----	---------------------	---------

24e. ENVIRONMENTAL CLEARANCE: YES

24g. U&amp;RR CLEARANCE: NO

24i. R/W CLEARANCE: YES

24k. SCOPING DOCUMENT: YES

24f. MATERIALS MEMO COMP: YES

24h. C&amp;S CLEARANCE: YES

24j. CUSTOMIZED SCHEDULE: YES

**25. DESCRIPTION OF REQUEST**

Increase budget.

**26. JUSTIFICATION OF REQUEST**

Additional construction funds are needed as a result of increased unit prices and increased quantities for the asphaltic concrete and AR-ACFC bid items. The milling quantity also increased because of an error in calculations at Stage III.

ICAP is included in this request.

Contingent on approval by MAG Regional Council on April 27, 2022.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 4/6/2022

**PRB APPROVED**


## 7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-12

**Route & MP:** SR 30 @ MP 0.0  
**Project Name:** SR 303L - SR 202L, SOUTH MOUNTAIN, PHASE I  
**Type of Work:** Utilities  
**County:** Maricopa  
**District:** Central  
**Schedule:**  
**Project:** H687601U TIP#: 8892  
**Project Manager:** Troy Sieglitz  
**Program Amount:** \$50,000  
**New Program Amount:** \$5,050,000  
**Requested Action:** Increase Budget.

---

SR 30: SR 303L - SR 202L South Mountain, Phase I

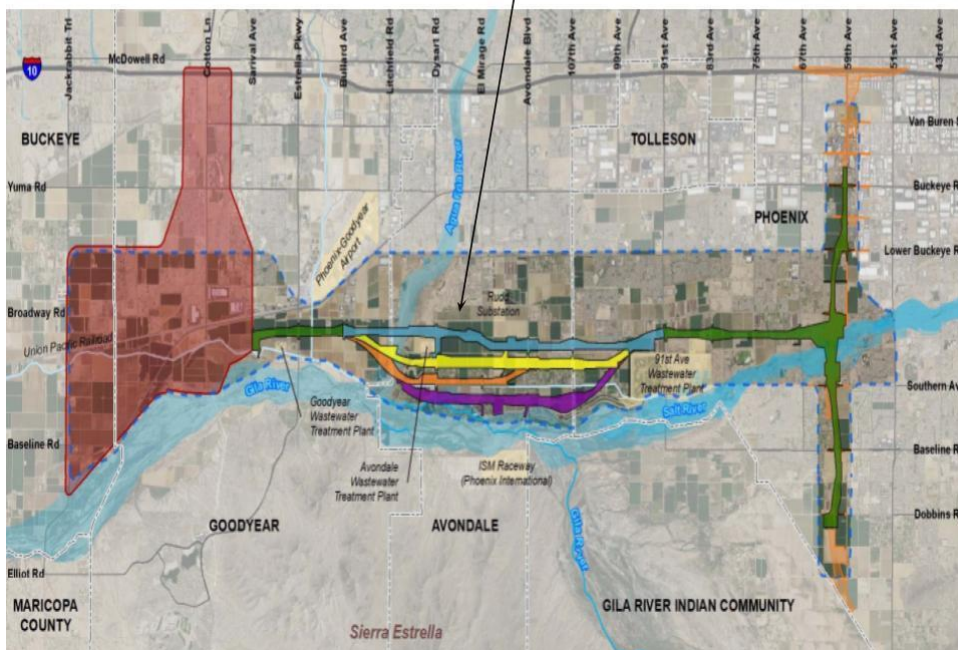

05

1. PRB Meeting Date: 3/8/2022

2. Teleconference: No

3. Form Date / 5. Form By:

3/8/2022

Troy Sieglitz

4. Project Manager / Presenter:

Troy Sieglitz @ (602) 712-2211

205 S 17th Ave, , -

6. Project Name:

SR 303L - SR 202L, SOUTH MOUNTAIN, PHASE I

7. Type of Work:

Utilities

8. CPSID:

JG1H

9. District:

Central

10. Route:

30

11. County:

Maricopa

12. Beg MP:

0.0

13. TRACS #:

H687601U

14. Len (Mi.):

24.0

15. Fed Id #:

NHPP888-0(0)A

16. Program Budget: \$50

17. Program Item #: 8892

18. Current Approved Program Budget:

\$50

18a. (+/-) Program Budget Request:

\$5,000

18b Total Program Budget After Request:

\$5,050

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
40208	\$50	.	

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
49922	\$5,000	.	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED:

NO

ADV:

NO



PROJECT FUNDING VERIFIED BY PM

**CHANGE IN:** 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: STAGE I

24e. ENVIRONMENTAL CLEARANCE: YES

24g. U&amp;RR CLEARANCE: NO

24i. R/W CLEARANCE: NO

24k. SCOPING DOCUMENT: NO

24f. MATERIALS MEMO COMP: NO

24h. C&amp;S CLEARANCE: NO

24j. CUSTOMIZED SCHEDULE: NO

**25. DESCRIPTION OF REQUEST**

Increase Budget

**26. JUSTIFICATION OF REQUEST**

The environmental decision document (Environmental Assessment) was approved on 11/06/2019 with a Finding of No Significant Impact (FONSI) allowing for long lead utility relocations to move forward for the SR 30, Tres Rios Freeway. Right-of-Way acquisition and funding is programmed over several years. This request will add FY 2022 funding for long lead utility relocations.

FY22 funding for right-of-way and utilities was updated and approved by the MAG Regional Council through a TIP Amendment on December 1, 2021.

DOT 22-839

Utilities: \$4525K

ICAP: \$475K

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 4/6/2022

**PRB APPROVED**

8. Listed below are the next regularly scheduled meetings of the Priority Planning Advisory Committee (PPAC). Meetings will be held by teleconference until further notice. Time, date, and location may change and will be announced at the time of the distribution of the agenda.
- Information Only

- May 4, 2022 10:00am Wednesday
- June 1, 2022 10:00am Wednesday
- June 29, 2022 10:00am Wednesday
- August 3, 2022 10:00am Wednesday
- August 31, 2022 10:00am Wednesday
- October 5, 2022 10:00am Wednesday
- November 2, 2022 10:00am Wednesday
- November 30, 2022 10:00am Wednesday

9. Adjourn Priority Planning Advisory Committee Meeting

#### **WEB LINKS FOR REFERENCE**

*Priority Programming*

[http://www.azdot.gov/MPD/Priority\\_Programming/Index.asp](http://www.azdot.gov/MPD/Priority_Programming/Index.asp)

*PPAC Meetings:*

[http://www.azdot.gov/MPD/Priority\\_Programming/PPAC/Index.asp](http://www.azdot.gov/MPD/Priority_Programming/PPAC/Index.asp)



**DRAFT MINUTES FOR THE  
ARIZONA DEPARTMENT OF TRANSPORTATION  
PRIORITY PLANNING ADVISORY COMMITTEE**

**Teleconference Meeting**

**Wednesday March 2, 2022 @ 10:00AM**

The meeting of the Priority Planning Advisory Committee (PPAC) was held on Wednesday March 2, 2022 @ 10:00AM with Chairman Paul Patane presiding.

Other committee members were present as follows:

Greg Byres, Steve Boschen, Brent Cain, Clem Ligocki, Barry Crockett, Don Kriz, John Morales, Elise Maza, and Jon Brodsky (Non-Voting).

**1. CALL TO ORDER**

Chairman Patane called the Priority Planning Advisory Committee meeting to order at 10:00AM.

**2. ROLL CALL**

Lynn Sugiyama conducted a roll call of the committee members. A full quorum was present.

**TITLE VI OF THE CIVIL RIGHTS ACT OF 1964, AS AMENDED**

- 3.** Chairman Patane stated that in accordance to the Title VI Civil Rights Act of 1964, and the Americans with Disabilities Act, ADOT will not discriminate on the basis of race, color, national origin, age, sex, or disability. If accommodations are requested, the public may contact someone on the PPAC Committee or the Civil Rights Office at 602-712-8964.

**CALL TO THE AUDIENCE**

Chairman Patane requested a call to the Audience for any comments or issues to be addressed, There

- 4.** were no comments from the audience. .

**APPROVAL OF PPAC MINUTES FROM THE 2/9/2022 MEETING**

Chairman Patane called for a motion to approve the PPAC minutes from the meeting on 2/9/2022.

- 5.** Steve Boschen made a motion to approve.

Don Kriz seconded the motion. The motion Motion carried unanimously.

**6. PROGRAM MONITORING REPORT**

The Program Monitoring Report was distributed to the Committee. Elise Maza stated that there were no comments to make on the Program Monitoring Report.

**7. 2022-2026 TRANSPORTATION FACILITIES CONSTRUCTION: DISCUSSION AND POSSIBLE ACTION ON PROJECT MODIFICATIONS & NEW PROJECTS**

7-1                    **Route & MP:**            Local  
                         **Route & MP:**            27TH AVE & THOMAS RD @ BNSF  
                         **Project Name:**            RAIL SAFETY PROJECT  
**Type of Work:** **County:**            Maricopa  
                         **District:**                    Central  
                         **Schedule:**  
                         **Project:**                    SR24501C TIP#: 102267  
                         **Project Manager:**            Jane Gauger  
**Program Amount: New**            \$0  
                         **Program Amount:**            \$1,350,000  
                         **Requested Action:**            Establish an 01C phase for civil construction work.

---

Item 7-1 was presented by: Jane Gauger  
Chairman called for a motion to approve Item 7-1.  
Steve Boschen made the motion to approve.  
Brent Cain seconded the motion. Motion carried unanimously.

---

---

7-2                    **Route & MP:**            Local  
                         **Project Name:**            27TH AVE & THOMAS RD @ BNSF  
                         **Type of Work:**            RAIL SAFETY PROJECT  
                         **County:**                    Maricopa  
                         **District:**                    Central  
                         **Schedule:**  
                         **Project:**                    SR24501X TIP#: 102267  
                         **Project Manager:**            Jane Gauger  
                         **Program Amount:**            \$0  
**New Program Amount:**            \$1,020,000  
                         **Requested Action:**            Establish an 01X phase for railroad construction.

---

Item 7-2 was presented by: Jane Gauger  
Chairman called for a motion to approve Item 7-2.  
Steve Boschen made the motion to approve.  
Barry Crockett seconded the motion. Motion carried unanimously.

---

---

7-3

**Route & MP:** SR 101L @ MP 8.0  
**Project Name:** CARDINAL WAY - SR 202 SAN TAN  
**Type of Work:** INSTALL CAMERAS  
**County:** Maricopa  
**District:** Central  
**Schedule:**  
**Project:** F048401X TIP#: 101787  
**Project Manager:** Joan Lovell  
**Program Amount:** \$0  
**New Program Amount:** \$372,000  
**Requested Action:** Establish Project.

---

**Item 7-3 was presented by: Joan Lovell**  
**Chairman called for a motion to approve Item 7-3.**  
**Brent Cain made the motion to approve.**  
**Greg Byres seconded the motion. Motion carried unanimously.**

---

---

7-4

**Route & MP:** Statewide  
**Project Name:** SMART SOFTWARE SUITE  
**Type of Work:** EXPAND & ENHANCE ANALYTIC TOOLS  
**County:** Maricopa  
**District:** Statewide  
**Schedule:**  
**Project:** M715502X TIP#: 101804  
**Project Manager:** John Roberts  
**Program Amount:** \$0  
**New Program Amount:** \$100,000  
**Requested Action:** Establish new project.

---

**Item 7-4 was presented by: John Roberts**  
**Chairman called for a motion to approve Item 7-4.**  
**Brent Cain made the motion to approve.**  
**Steve Boschen seconded the motion. Motion carried unanimously.**

---

---

7-5

**Route & MP:** I-10 @ MP 122.0  
**Project Name:** JACKRABBIT TRAIL TI  
**Type of Work:** SCOPING (DCR/Env Doc)  
**County:** Maricopa  
**District:** Central  
**Schedule:**  
**Project:** F048601L TIP#: 102988  
**Project Manager:** Olivier Mirza  
**Program Amount:** \$0  
**New Program Amount:** \$1,500,000  
**Requested Action:** Establish a Scoping Project.

---

**Item 7-5 was presented by: Olivier Mirza**  
**Chairman called for a motion to approve Item 7-5.**  
**Steve Boschen made the motion to approve.**  
**Greg Byres seconded the motion. Motion carried unanimously**

---

---

7-6

**Route & MP:** SR 80 @ MP 298.8  
**Project Name:** SAN PEDRO RIVER BRIDGE  
**Type of Work:** CONSTRUCT BRIDGE REPLACEMENT  
**County:** Cochise  
**District:** Southcentral  
**Schedule:** FY 2022  
**Project:** H893701C TIP#: 6807  
**Project Manager:** Olivier Mirza  
**Program Amount:** \$8,500,000  
**New Program Amount:** \$10,500,000  
**Requested Action:** Increase Construction Budget.

---

**Item 7-6 was presented by: Olivier Mirza**  
**Chairman called for a motion to approve Item 7-6.**  
**Steve Boschen made the motion to approve.**  
**Greg Byres seconded the motion. Motion carried unanimously.**

---

---

7-7	AIRPORT PROGRAM: GRANT MANAGER:	Glendale Municipal Airport Sonia Pizano
	REQUESTED ACTION:	To establish a new airport project in the amount of \$154,287.00. This will be added to the list of the FY 22 Airport Capital Improvement Program.

---

Item 7-7 was presented by: Sonia Pizano  
Chairman called for a motion to approve Item 7-7.  
Don Kriz made the motion to approve.  
Greg Byres seconded the motion. Motion carried unanimously.

---

---

#### 7. ADDENDUM TO PPAC AGENDA - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-8	Route & MP:	Statewide
	Project Name:	EV INFRASTRUCTURE DEPLOYMENT PLAN
	Type of Work:	Planning Project
	County:	Statewide
	District:	Statewide
	Schedule:	
	Project:	PEV2201P, TIP#: 103191
	Project Manager:	Thor Anderson
	Program Amount:	\$0
	New Program Amount:	\$500,000
	Requested Action:	Establish the initial plan to fund the electric vehicle charging station program.

---

Item 7-8 was presented by: Thor Anderson  
Chairman called for a motion to approve Item 7-8.  
Steve Boschen made the motion to approve.  
Greg Byres seconded the motion. Motion carried unanimously

---

---

## **8. FUTURE MEETINGS**

Listed below are the next regularly scheduled meetings of the Priority Planning Advisory Committee (PPAC). Meetings will be held in the ADOT Board Room, however, times, dates, and location may change and will be announced at the time of the distribution of the agenda.

March 30, 2022 on Wednesday at 10am.  
May 4, 2022 on Wednesday at 10am.  
June 1, 2022 on Wednesday at 10am.  
June 29, 2022 on Wednesday at 10am.  
August 3, 2022 on Wednesday at 10am.  
August 31, 2022 on Wednesday at 10am.  
October 5, 2022 on Wednesday at 10am.  
November 2, 2022 on Wednesday at 10am.  
November 30, 2022 on Wednesday at 10am.

## **9. ADJOURN PRIORITY PLANNING ADVISORY COMMITTEE MEETING**

**Chairman Patane announced the adjournment of the meeting.  
Meeting adjourned at 10:27am.**

---

---

### **WEB LINKS FOR REFERENCE**

*Priority Programming Website:*

<https://azdot.gov/about/boards-and-committees/priority-planning-advisory-committee>

*PPAC Meeting Dates:*

<https://azdot.gov/about/boards-and-committees/priority-planning-advisory-committee/meeting-schedule-ppac>
