



**PRIORITY PLANNING ADVISORY COMMITTEE  
(PPAC)**

**AGENDA**

**MEETING OF:**

**Wednesday, December 2, 2020**



## ADOT’S NONDISCRIMINATION NOTICE TO THE PUBLIC

The Arizona Department of Transportation (ADOT) hereby gives public notice that it is the Agency’s policy to assure full compliance with Title VI of the Civil Rights Act of 1964, Title II of the Americans with Disabilities Act of 1990 (ADA), and other related authorities in all of its programs and activities.

ADOT’s Title VI and ADA Programs require that no person shall, on the grounds of race, color, national origin, or disability, be excluded from participation in, be denied the benefits of, or be otherwise subjected to discrimination under any program or activity.

Any person, who believes his/her Title VI or ADA rights have been violated, may file a complaint. Any such complaint must be in writing and filed with the ADOT Civil Rights Office within one hundred eighty (180) days following the date of the alleged discriminatory occurrence. For additional information about ADOT’s Civil Rights programs and the procedures to file a complaint contact ADOT Civil Rights Office via the information listed below:

## AVISO PÚBLICO DE LA LEY DE NO-DISCRIMINACIÓN DE ADOT

El Departamento de Transporte del Estado de Arizona (ADOT) informa al público que esta agencia tiene como regla asegurar el cumplimiento total del Título VI de la Ley de los Derechos Civiles de 1964, del Título II de la Ley de ciudadanos Americanos con Discapacidades de 1990 (ADA) y otras normas relacionadas con todos sus programas y actividades.

Los programas del Título VI y ADA de ADOT exigen que a ninguna persona se le excluya de participar, se le nieguen beneficios o de ninguna otra manera sea sujeta a discriminación en ningún programa o actividad de ADOT por motivo de raza, color, país de origen, o discapacidad.

Cualquier persona que crea que se han violado sus derechos bajo el Título VI o el ADA, puede presentar una queja. Esta queja debe presentarse por escrito a la Oficina de Derechos Civiles de ADOT dentro de ciento ochenta (180) días a partir de la fecha en que se alega que ocurrió la discriminación. Para recibir más información sobre los programas de Derechos Civiles de ADOT y los procedimientos para presentar una queja, por favor póngase en contacto con la Oficina de Derechos Civiles de ADOT a través la información que aparece abajo:

**FELICIA BELTRAN**  
TITLE VI NONDISCRIMINATION  
PROGRAM COORDINATOR  
[FBELTRAN@AZDOT.GOV](mailto:FBELTRAN@AZDOT.GOV)  
**KRYSTAL SMITH**  
ADA/NONDISCRIMINATION  
PROGRAM COORDINATOR  
[KSMITH2@AZDOT.GOV](mailto:KSMITH2@AZDOT.GOV)

**ADOT Civil Rights Office**  
206 S. 17th Avenue, Mail Drop 155-A  
Phoenix, AZ 85007  
602.712.8946  
602.239.6257 FAX  
[azdot.gov](http://azdot.gov)

**ARIZONA DEPARTMENT OF TRANSPORTATION  
MULTIMODAL PLANNING DIVISION  
OFFICE MEMO**

TO: PRIORITY PLANNING ADVISORY COMMITTEE MEMBERS

DALLAS HAMMIT  
KRISTINE WARD  
STEVE BOSCHEN  
BRENT CAIN  
CLEMENC LIGOCKI  
TIM LANE  
BARRY CROCKETT  
TIM TAIT (NON-VOTING)  
DON KRIZ

FROM: Chariman Gregory Byres

SUBJECT: PRIORITY PLANNING ADVISORY COMMITTEE MEETING (PPAC)

Pursuant to the A.R.S. 28-6951(B), the ADOT Director has appointed the members of the Priority Planning Advisory Committee (PPAC) to develop the Five Year Transportation Facilities Construction Program. This meeting is scheduled, pursuant to 28-6951(C4), to review the Program and make changes and schedule new projects into the adopted Five Year Transportation Facilities Construction Program.

Pursuant to Title VI of the Civil Rights Act of 1964, and the Americans with Disabilities Act (ADA), ADOT does not discriminate on the basis of race, color, national origin, age, sex or disability. Persons who require a reasonable accommodation based on language or disability should contact ADOT's Civil Rights Office at 602-712-8946 or at <civilrightsoffice@azdot.gov>. Requests should be made as early as possible to ensure the State has an opportunity to address the accommodation.

The meeting of the Arizona Department of Transportation, Priority Planning Advisory Committee (PPAC) will be held on Wednesday December 2nd, 2020 at 10:00AM. To access the PPAC meeting through the Internet, please go to < [meet.google.com/iuy-mohw-uki](https://meet.google.com/iuy-mohw-uki) >. To access the meeting by phone, please call +1 530-728-0224 PIN: 579 884 373 #.

**AGENDA:**

1. Call to Order	Chairman
2. Roll Call	Information Only
3. Title VI: The Civil Rights Act of 1964, as Amended	Information Only
4. Call to Audience	Information Only
5. Approval of the PPAC Minutes on 11/4/2020	Discussion and Possible Action    Page 23
6. Program Monitoring Report	Information & Discussion

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-1	<b>Route &amp; MP:</b>	I-40 @ MP 109.0
	<b>Project Name:</b>	ANVIL ROCK RD TI UP
	<b>Type of Work:</b>	REPLACE BRIDGE DECK
	<b>County:</b>	Yavapai
	<b>District:</b>	Northwest
	<b>Schedule:</b>	FY 2021
	<b>Project:</b>	F025401C TIP#: 9110
	<b>Project Manager:</b>	Shantala Ramaiah
	<b>Program Amount:</b>	\$3,000,000
	<b>New Program Amount:</b>	\$0
	<b>Requested Action:</b>	Defer project.

---



**06**

1. PRB Meeting Date: 11/24/2020

2. Teleconference: No

3. Form Date / 5. Form By:

11/24/2020

Shantala Ramaiah

4. Project Manager / Presenter:

Shantala Ramaiah @

- 4983 PROJECT MANAGEMENT

6. Project Name:

ANVIL ROCK RD TI UP

7. Type of Work:

REPLACE BRIDGE DECK

8. CPSID:

[LX10](#)

9. District:

Northwest

10. Route:

40

11. County:

Yavapai

12. Beg MP:

109.0

13. TRACS #:

F025401C ?

14. Len (Mi.):

1.0

15. Fed Id #:

NHPP040-B(230)T

16. Program Budget: \$3,000

17. Program Item #: 9110

18. Current Approved Program Budget:

\$3,000

18a. (+/-) Program Budget Request:

(\$3,000)

18b Total Program Budget After Request:

\$0

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
9110	\$3,000	Anvil Rock Rd TI UP	

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
76221	(\$3,000)	BRIDGE REPLACEMENT & REHABILITATION	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR: 21

22. CURRENT BID READY:

23. CURRENT ADV DATE: 12/18/2020

**CHANGE REQUEST/NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR: 22

22A. REQUEST BID READY:

23A. REQUEST ADV DATE: 11/18/2021

20. JPA #'s:

SIGNED:

NO

ADV:

NO

**CHANGE IN:**

24a. PROJECT NAME:

NO

24b. TYPE OF WORK:

NO

24c. SCOPE:

NO

24d. CURRENT STAGE:

STAGE V

24e. ENVIRONMENTAL CLEARANCE:

YES

24f. MATERIALS MEMO COMP:

YES

24g. U&amp;RR CLEARANCE:

YES

24h. C&amp;S CLEARANCE:

YES

24i. R/W CLEARANCE:

YES

24j. CUSTOMIZED SCHEDULE:

YES

24k. SCOPING DOCUMENT:

YES

**25. DESCRIPTION OF REQUEST**

Defer project.

**26. JUSTIFICATION OF REQUEST**

Funding is needed for a higher priority project. This project is being deferred to FY22.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN SCHEDULE

CHANGE IN FY

CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED

SUBJECT TO PPAC APPROVAL - 12/2/2020



7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-2	<b>Route &amp; MP:</b>	I-40 @ MP 122.0
	<b>Project Name:</b>	E SELIGMAN TI OP, EB/ WB
	<b>Type of Work:</b>	CONSTRUCT BRIDGE DECK REHABILITATION
	<b>County:</b>	Yavapai
	<b>District:</b>	Northwest
	<b>Schedule:</b>	FY 2021
	<b>Project:</b>	F016101C TIP#: 8374
	<b>Project Manager:</b>	Kirstin Huston
	<b>Program Amount:</b>	\$6,500,000
	<b>New Program Amount:</b>	\$0
	<b>Requested Action:</b>	Defer project.

---





**07**

1. PRB Meeting Date: 11/24/2020

2. Teleconference: No

3. Form Date / 5. Form By:

11/24/2020

Lee Makler

4. Project Manager / Presenter:

Kirstin Huston @ (602) 712-8618

1655 W Jackson St, 121F - 4983 PROJECT MANAGEMENT

6. Project Name:

E SELIGMAN TI OP, EB/ WB

7. Type of Work:

CONSTRUCT BRIDGE DECK REHABILITATION

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
<a href="#">DE10</a>	Northwest	40	Yavapai	122.0	F016101C ?	1.0	NHPP040-B(229)T

16. Program Budget: \$6,500

17. Program Item #: 8374

18. Current Approved Program Budget:

\$6,500

18a. (+/-) Program Budget Request:

(\$6,500)

18b Total Program Budget After Request:

\$0

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
8374	\$0	E Seligman TI OP, EB/WB	BRIDGE INSPECTION & INVENTORY

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
76221	(\$6,500)	BRIDGE REPLACEMENT & REHABILITATION	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR: 21

22. CURRENT BID READY:

23. CURRENT ADV DATE: 6/18/2021

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR: 22

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s: SIGNED: NO ADV: NO

<b>CHANGE IN:</b>	24a. PROJECT NAME:	NO	24b. TYPE OF WORK:	NO	24c. SCOPE:	NO	24d. CURRENT STAGE:	STAGE IV
-------------------	--------------------	----	--------------------	----	-------------	----	---------------------	----------

24e. ENVIRONMENTAL CLEARANCE: YES

24f. MATERIALS MEMO COMP: NO

24g. U&amp;RR CLEARANCE: YES

24h. C&amp;S CLEARANCE: NO

24i. R/W CLEARANCE: YES

24j. CUSTOMIZED SCHEDULE: YES

24k. SCOPING DOCUMENT: YES

**25. DESCRIPTION OF REQUEST**

Defer project

**26. JUSTIFICATION OF REQUEST**

Funding is needed for a higher priority project. This project is being deferred to FY22.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN FY  
CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 12/2/2020



7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-3	<b>Route &amp; MP:</b>	I-40 @ MP 288.0
	<b>Project Name:</b>	HERMOSA DRIVE UP
	<b>Type of Work:</b>	CONSTRUCT BRIDGE REHABILITATION
	<b>County:</b>	Navajo
	<b>District:</b>	Northeast
	<b>Schedule:</b>	FY 2021
	<b>Project:</b>	F023001C TIP#: 9116
	<b>Project Manager:</b>	Sandy Thoms
	<b>Program Amount:</b>	\$3,000,000
	<b>New Program Amount:</b>	\$0
	<b>Requested Action:</b>	Defer project.

---





**08**

1. PRB Meeting Date: 11/24/2020

2. Teleconference: No

3. Form Date / 5. Form By:

11/24/2020

Lee Makler

4. Project Manager / Presenter:

Sandy Thoms @

,, - 4983 PROJECT MANAGEMENT

6. Project Name:

HERMOSA DRIVE UP

7. Type of Work:

CONSTRUCT BRIDGE REHABILITATION

8. CPSID:

[LY10](#)

9. District:

Northeast

10. Route:

40

11. County:

Navajo

12. Beg MP:

288.0

13. TRACS #:

F023001C ?

14. Len (Mi.):

1.0

15. Fed Id #:

NHPP040-D(241)T

16. Program Budget: \$3,000

17. Program Item # 9116

18. Current Approved Program Budget:

\$3,000

18a. (+/-) Program Budget Request:

(\$3,000)

18b Total Program Budget After Request:

\$0

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
9116	\$2,000	Hermosa Drive UP	BRIDGE INSPECTION & INVENTORY

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
76221	(\$3,000)	BRIDGE REPLACEMENT & REHABILITATION	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR: 21

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR: 22

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED:

NO

ADV:

NO

**CHANGE IN:**

24a. PROJECT NAME:

NO

24b. TYPE OF WORK:

NO

24c. SCOPE:

NO

24d. CURRENT STAGE:

STAGE IV

24e. ENVIRONMENTAL CLEARANCE:

YES

24f. MATERIALS MEMO COMP:

YES

24g. U&amp;RR CLEARANCE:

YES

24h. C&amp;S CLEARANCE:

NO

24i. R/W CLEARANCE:

YES

24j. CUSTOMIZED SCHEDULE:

YES

24k. SCOPING DOCUMENT:

YES

**25. DESCRIPTION OF REQUEST**

Defer project

**26. JUSTIFICATION OF REQUEST**

Funding is needed for a higher priority project. This project is being deferred to FY22.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN FY

CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED


SUBJECT TO PPAC APPROVAL - 12/2/2020



7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-4	<b>Route &amp; MP:</b>	I--15 @ MP 9.6
	<b>Project Name:</b>	VIRGIN RIVER BRIDGE NO 1
	<b>Type of Work:</b>	BRIDGE REPLACEMENT
	<b>County:</b>	Mohave
	<b>District:</b>	Northcentral
	<b>Schedule:</b>	FY 2021
	<b>Project:</b>	H876001C TIP#: 10219
	<b>Project Manager:</b>	Jennifer Acuna
	<b>Program Amount:</b>	\$60,000,000
	<b>New Program Amount:</b>	\$73,000,000
	<b>Requested Action:</b>	Increase budget

---

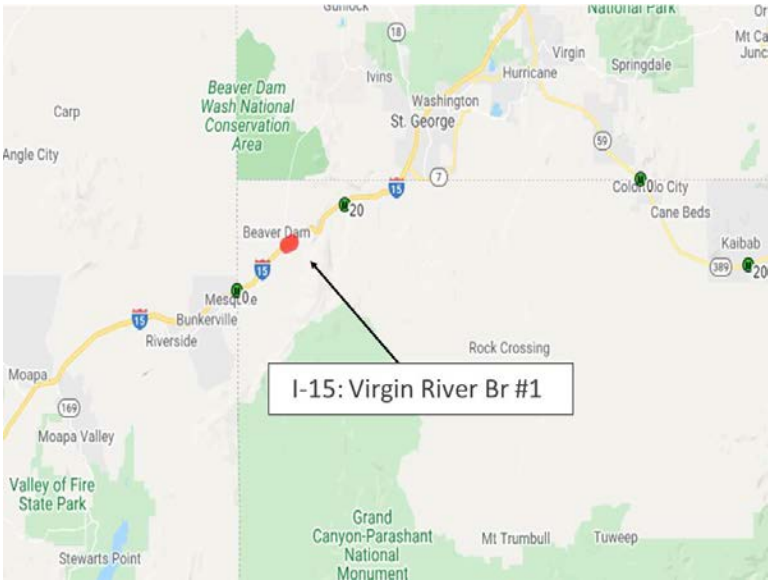

**09**

1. PRB Meeting Date: 11/24/2020

2. Teleconference: No

3. Form Date / 5. Form By:

11/24/2020

Lee Makler

4. Project Manager / Presenter:

Jennifer Acuna @ (602) 712-8336

205 S 17th Ave, 295, 614E - 4983 PROJECT MANAGEMENT

6. Project Name:

VIRGIN RIVER BRIDGE NO 1

7. Type of Work:

BRIDGE REPLACEMENT

8. CPSID:

[FA1N](#)

9. District:

Northcentral

10. Route:

15

11. County:

Mohave

12. Beg MP:

9.6

13. TRACS #:

H876001C

14. Len (Mi.):

1.0

15. Fed Id #:

NHPP015-A(216)S

16. Program Budget: \$60,000

17. Program Item #: 10219

18. Current Approved Program Budget:

\$60,000

18a. (+/-) Program Budget Request:

\$13,000

18b Total Program Budget After Request:

\$73,000

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
10219	\$60,000	VIRGIN RIVER BRIDGE NUMBER 1	BRIDGE REPLACEMENT & REHABILITATION

**CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
76221	\$13,000	BRIDGE REPLACEMENT & REHABILITATION	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR: 21

22. CURRENT BID READY:

23. CURRENT ADV DATE: 11/2/2020

**CHANGE REQUEST NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED:

NO

ADV:

NO

**CHANGE IN:**

24a. PROJECT NAME:

NO

24b. TYPE OF WORK:

NO

24c. SCOPE:

NO

24d. CURRENT STAGE:

STAGE IV

24e. ENVIRONMENTAL CLEARANCE:

NO

24f. MATERIALS MEMO COMP:

NO

24g. U&amp;RR CLEARANCE:

YES

24h. C&amp;S CLEARANCE:

NO

24i. R/W CLEARANCE:

NO

24j. CUSTOMIZED SCHEDULE:

YES

24k. SCOPING DOCUMENT:

YES

**25. DESCRIPTION OF REQUEST**

Increase budget

**26. JUSTIFICATION OF REQUEST**

The latest construction estimates from 2 independent sources and the State are higher than the programmed amount, therefore additional funding is needed to cover the difference. Increasing the funding for the construction phase would allow the State to either accept a GMP from the CMAR or advertise for bids from a contractor.

ICAP is included.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN BUDGET

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED

SUBJECT TO PPAC APPROVAL - 12/2/2020



7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-5	<b>Route &amp; MP:</b>	SR 89A @ MP 374.0
	<b>Project Name:</b>	SR-89A & SR-179
	<b>Type of Work:</b>	RIGHT TURN SLIP LANES
	<b>County:</b>	Coconino
	<b>District:</b>	Northcentral
	<b>Schedule:</b>	
	<b>Project:</b>	F020601D, TIP: 101184
	<b>Project Manager:</b>	Jennifer Acuna
	<b>Program Amount:</b>	\$506,000
	<b>New Program Amount:</b>	\$506,000
	<b>Requested Action:</b>	Change of scope. Change Type of Work.

---



**11**

1. PRB Meeting Date: 11/17/2020

2. Teleconference: No

3. Form Date / 5. Form By:

11/19/2020

Jennifer Acuna

4. Project Manager / Presenter:

Jennifer Acuna @ (602) 712-8336

205 S 17th Ave, 295, 614E - 4983 PROJECT MANAGEMENT

6. Project Name:

SR-89A &amp; SR-179

7. Type of Work:

RIGHT TURN SLIP LANES

8. CPSID:

[UW10](#)

9. District:

Northcentral

10. Route:

89A

11. County:

Coconino

12. Beg MP:

374.0

13. TRACS #:

F020601D

14. Len (Mi.):

1.0

15. Fed Id #:

STGBA89-A(210)T

16. Program Budget: \$506

17. Program Item #: 101184

18. Current Approved Program Budget:

\$506

18a. (+/-) Program Budget Request:

\$0

18b Total Program Budget After Request:

\$506

**CURRENTLY APPROVED:****19. BUDGET ITEMS:**

Item #	Amount	Description	Comments
OTHR19	\$253	.	City of Sedona share.
73319	\$253	.	ADOT share.

**CHANGE / REQUEST:****19A. BUDGET ITEMS:****CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST/NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s: 18-0006995-I

SIGNED: YES

ADV: YES

**CHANGE IN:** 24a. PROJECT NAME: NO 24b. TYPE OF WORK: YES 24c. SCOPE: YES 24d. CURRENT STAGE: NOT APPLICABLE

24e. ENVIRONMENTAL CLEARANCE:

NO

24f. MATERIALS MEMO COMP:

YES

24g. U&amp;RR CLEARANCE:

NO

24h. C&amp;S CLEARANCE:

NO

24i. R/W CLEARANCE:

NO

24j. CUSTOMIZED SCHEDULE:

NO

24k. SCOPING DOCUMENT:

YES

**25. DESCRIPTION OF REQUEST**

Change scope.

Change Type of Work.

**26. JUSTIFICATION OF REQUEST**

This is a Minor Program Project.

After calibrating the roundabout simulation model, the design team agreed that the original scope would not produce the desired outcome of reducing queueing and congestion at the roundabout. Therefore the project team agreed to change the scope of work and extend the project limits. The revised scope of work will consist of minor pavement rehabilitation to accommodate modernized pavement markings and some potential signage updates. The project limits will be extended to include the SR 89A and Brewer Rd roundabout just west of the SR179 intersection. Due to the change in the scope of work the type of work will also change to; "Minor pavement & pavement marking rehab".

No additional funds are needed at this time.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

CHANGE IN SCOPE

CHANGE IN TYPE OF WORK

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED


SUBJECT TO PPAC APPROVAL - 12/2/2020



7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-6	<b>Route &amp; MP:</b>	SR 87 @ MP 132
	<b>Project Name:</b>	SR 87, Coolidge & B-19, Nogales
	<b>Type of Work:</b>	UPGRADE TRAFFIC SIGNAL CABINETS
	<b>County:</b>	Pinal
	<b>District:</b>	Southcentral
	<b>Schedule:</b>	
	<b>Project:</b>	F036801C, TIP#: 102244
	<b>Project Manager:</b>	James Gomes
	<b>Program Amount:</b>	\$0
	<b>New Program Amount:</b>	\$180,000
	<b>Requested Action:</b>	Establish New Project.

---

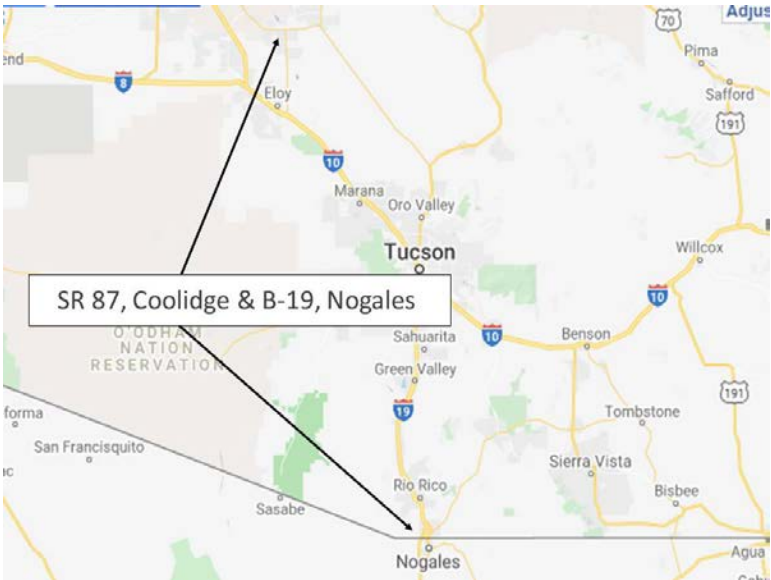

04

## Project Review Board (PRB) Request Form - Version 4.0

1. PRB Meeting Date: 11/3/2020



2. Teleconference: (520) 388-4231

3. Form Date / 5. Form By:

11/9/2020

James Gomes

4. Project Manager / Presenter:

James Gomes @ (520) 388-4231

1221 S 2nd Ave, , T100 - 6500 OPERATIONAL TRAFFIC &amp; SAFETY ADMINISTRAT

6. Project Name:

SR 87, Coolidge &amp; B-19, Nogales

7. Type of Work:

UPGRADE TRAFFIC SIGNAL CABINETS

8. CPSID: 9. District: 10. Route: 11. County: 12. Beg MP: 13. TRACS #: 14. Len (Mi.): 15. Fed Id #:

- Southcentral 87 Pinal 132 F036801C ?

16. Program Budget: \$0

17. Program Item #: 102244

18. Current Approved Program Budget:

\$0

18a. (+/-) Program Budget Request:

\$180

18b Total Program Budget After Request:

\$180

**CURRENTLY APPROVED:****19. BUDGET ITEMS:****CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
78821	\$180	TSM&O	TSMO Subprogram

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST/NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED:

NO

ADV:

NO

**CHANGE IN:** 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: NOT APPLICABLE

24e. ENVIRONMENTAL CLEARANCE:

NO

24f. MATERIALS MEMO COMP:

NO

24g. U&amp;RR CLEARANCE:

NO

24h. C&amp;S CLEARANCE:

NO

24i. R/W CLEARANCE:

NO

24j. CUSTOMIZED SCHEDULE:

NO

24k. SCOPING DOCUMENT:

NO

**25. DESCRIPTION OF REQUEST**

Establish New Project

**26. JUSTIFICATION OF REQUEST**

The South Central Traffic Operations (Unit 6543) requests to upgrade 12 TS-1 signal cabinets with TS-2, Type 1 signal cabinets along SR-87 in City of Coolidge and B-19 in the City of Nogales. This will include adding conductors and any detection, preemption or loops that need to be rewired along the same corridor. This work is necessary since the cabinets currently installed at each location are outdated equipment. They are all 10 to 15+ years old and require replacement for optimal functionality with the new communication equipment that will be installed. When these older cabinets are knocked down, replacing them with the same type, TS-1, requires more than eight hours for the signal techs to rewire to ensure functionality. With the requested TS-2 replacement cabinets, no wiring is needed, as all programming is done through the controller, allowing the technician to make adjustments more efficiently.

This project involves utilizing ADOT manpower to remove the existing TS-1 signal cabinets and replace with the new TS-2, Type I signal cabinets at the 6 intersections along SR-87 in Coolidge and 6 intersections along B-19 in Nogales.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

ESTABLISH A NEW PROJECT

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 12/2/2020

**PRB APPROVED**




## 7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-7

**Route & MP:** I-10 @ MP 131  
**Project Name:** AVONDALE BLVD - I-17  
**Type of Work:** PAVEMENT REHABILITATION  
**County:** Maricopa  
**District:** Central  
**Schedule:** FY 20 2022  
**Project:** F023301C TIP#: 100335  
**Project Manager:** Bharat Kandel  
**Program Amount:** \$0  
**New Program Amount:** \$14,600,000  
**Requested Action:** Establish FY21 Project.

---

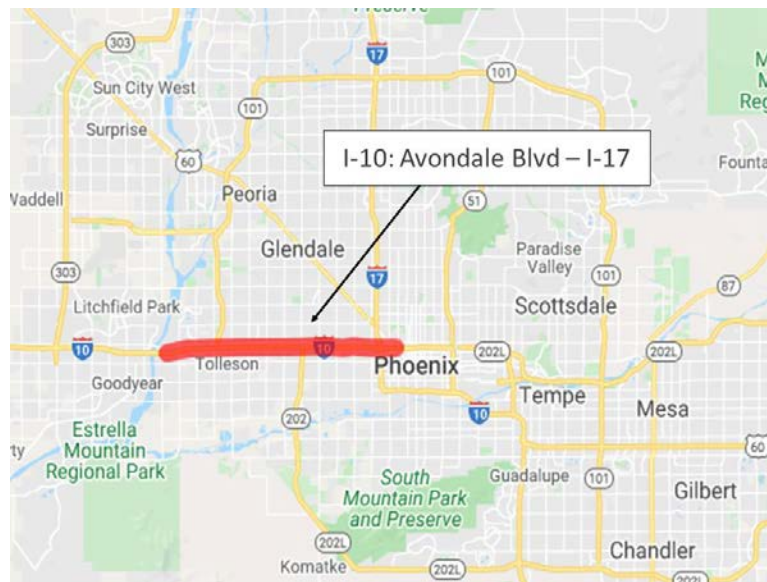

**07**

1. PRB Meeting Date: 11/17/2020

2. Teleconference: No

3. Form Date / 5. Form By:

11/19/2020

Bharat Kandel

4. Project Manager / Presenter:

Bharat Kandel @ (602) 712-8736

205 S 17th Ave, , EM01 - 4983 PROJECT MANAGEMENT

6. Project Name:

AVONDALE BLVD - I-17

7. Type of Work:

PAVEMENT REHABILITATION

8. CPSID:	9. District:	10. Route:	11. County:	12. Beg MP:	13. TRACS #:	14. Len (Mi.):	15. Fed Id #:
<a href="#">SF10</a>	Central	10	Maricopa	131	F023301C ?	13	010-B(220)T

16. Program Budget: \$0

17. Program Item #: 100335

18. Current Approved Program Budget:

\$0

18a. (+/-) Program Budget Request:

\$14,600

18b Total Program Budget After Request:

\$14,600

**CURRENTLY APPROVED:****19. BUDGET ITEMS:****CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
72521	\$14,600	PRESERVATION	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR: 2022

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST/NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR: 2021

22A. REQUEST BID READY:

23A. REQUEST ADV DATE: 1/12/2021

20. JPA #'s: SIGNED: NO ADV: NO

<b>CHANGE IN:</b>	24a. PROJECT NAME:	NO	24b. TYPE OF WORK:	NO	24c. SCOPE:	NO	24d. CURRENT STAGE:	STAGE IV
-------------------	--------------------	----	--------------------	----	-------------	----	---------------------	----------

24e. ENVIRONMENTAL CLEARANCE: NO

24f. MATERIALS MEMO COMP: YES

24g. U&amp;RR CLEARANCE: NO

24h. C&amp;S CLEARANCE: NO

24i. R/W CLEARANCE: YES

24j. CUSTOMIZED SCHEDULE: YES

24k. SCOPING DOCUMENT: YES

**25. DESCRIPTION OF REQUEST**

Establish FY21 Project.

**26. JUSTIFICATION OF REQUEST**

In the 2020-24 ADOT Five Year Program, construction of the project was shown in ADOT FY21, whereas in the 2021-25 ADOT Five Year Program, construction is shown in ADOT FY22. The project includes improvements in lane/stripping configurations on WB I-10 between 67th Ave and Avondale Blvd and SB 101L to I-10 WB Ramp, which will significantly benefit the travelling public, if the project is constructed sooner (FY21) than in FY22.

MAG has performed the regional Air Quality Conformity network model run for the proposed lane configurations. Conformity finding and MAG TIP amendment is scheduled to be in the Agenda of December 2, 2020 MAG Regional Council Meeting for approval.

ICAP is included.

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

ESTABLISH A NEW PROJECT

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
 SUBJECT TO PPAC APPROVAL - 12/2/2020



7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-8	<b>Route &amp; MP:</b>	Regionwide
	<b>Project Name:</b>	DMS MESSAGE FUNCTIONALITY
	<b>Type of Work:</b>	ENHANCE DISPLAY CAPABILITY
	<b>County:</b>	Maricopa
	<b>District:</b>	Central
	<b>Schedule:</b>	
	<b>Project:</b>	F035501X TIP#: 102251
	<b>Project Manager:</b>	John Roberts
	<b>Program Amount:</b>	\$0
	<b>New Program Amount:</b>	\$77,000
	<b>Requested Action:</b>	Establish new project.

---

**02**

1. PRB Meeting Date: 11/17/2020

2. Teleconference: No

3. Form Date / 5. Form By:

11/20/2020

John Roberts

4. Project Manager / Presenter:

John Roberts @ (602) 712-3830

2302 W Durango St, 078R - 6003 SYSTEMS TECHNOLOGY

6. Project Name:

DMS MESSAGE FUNCTIONALITY

7. Type of Work:

ENHANCE DISPLAY CAPABILITY

8. CPSID: 9. District: 10. Route: 11. County: 12. Beg MP: 13. TRACS #: 14. Len (Mi.): 15. Fed Id #:  
 - Phoenix Maricopa F035501X ?

16. Program Budget: \$0

17. Program Item #: 102251

18. Current Approved Program Budget:

\$0

18a. (+/-) Program Budget Request:

\$77

18b Total Program Budget After Request:

\$77

**CURRENTLY APPROVED:****19. BUDGET ITEMS:****CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
78821/1 006	\$77	.	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST/NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR: 21

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED: NO

ADV: NO

**PROJECT FUNDING VERIFIED BY PM**

**CHANGE IN:** 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: NOT APPLICABLE

24e. ENVIRONMENTAL CLEARANCE:

NO

24f. MATERIALS MEMO COMP:

NO

24g. U&amp;RR CLEARANCE:

NO

24h. C&amp;S CLEARANCE:

NO

24i. R/W CLEARANCE:

NO

24j. CUSTOMIZED SCHEDULE:

NO

24k. SCOPING DOCUMENT:

NO

**25. DESCRIPTION OF REQUEST**

Establish new project

**26. JUSTIFICATION OF REQUEST**

This request covers all costs for software implementation of Color Dynamic Message features and processes in traffic operations statewide. This includes color features on existing and future of DMSs, DMS message text to graphic automatic interchangeability, symbol library for use on Dynamic Message Signs, user interface for Traffic Operations and standard processes for use.

Materials: \$70K

ICAP: \$7K

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

ESTABLISH A NEW PROJECT

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
 SUBJECT TO PPAC APPROVAL - 12/2/2020

**PRB APPROVED**

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-9	<b>Route &amp; MP:</b>	Regionwide
	<b>Project Name:</b>	MAG REGION FWYS / IRU OPERATIONS
	<b>Type of Work:</b>	INCIDENT RESPONSE UNIT CONGESTION MITIGATION
	<b>County:</b>	Maricopa
	<b>District:</b>	
	<b>Schedule:</b>	
	<b>Project:</b>	M716401X TIP#: 102239
	<b>Project Manager:</b>	Mark Brown
	<b>Program Amount:</b>	\$0
	<b>New Program Amount:</b>	\$493,000
	<b>Requested Action:</b>	Establish new project.

---

**04**
1. PRB Meeting Date: 11/17/2020 ☒ 2. Teleconference: 602-712-7688
3. Form Date / 5. Form By:

11/24/2020

Jennifer Vanvenroy

4. Project Manager / Presenter:

Mark Brown @

Traffic Operations Center - 6304 INCIDENT RESPONSE UNIT

6. Project Name:

MAG REGION FWYS / IRU OPERATIONS

7. Type of Work:

INCIDENT RESPONSE UNIT CONGESTION MITIGATION

8. CPSID: 9. District: 10. Route: 11. County: 12. Beg MP: 13. TRACS #: 14. Len (Mi.): 15. Fed Id #:  
- Phoenix 888 Maricopa M716401X ?
16. Program Budget: \$017. Program Item #: 10223918. Current Approved Program Budget:

\$0

18a. (+/-) Program Budget Request:

\$493

18b Total Program Budget After Request:

\$493

**CURRENTLY APPROVED:****19. BUDGET ITEMS:****CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
OTHR21	\$465		CMAQ Funds-MAG ID: 15527 MAG TIP ID: DOT20-814Ph1
78821	\$28	TSM&O	State match

**CURRENT SCHEDULE:**21. CURRENT FISCAL YEAR:22. CURRENT BID READY:23. CURRENT ADV DATE:**CHANGE REQUEST/NEW SCHEDULE:**21A. REQUEST FISCAL YEAR:22A. REQUEST BID READY:23A. REQUEST ADV DATE:20. JPA #'s:SIGNED: NOADV: NO**PROJECT FUNDING VERIFIED BY PM**
**CHANGE IN:** 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: NOT APPLICABLE
24e. ENVIRONMENTAL CLEARANCE:

NO

24f. MATERIALS MEMO COMP:

NO

24g. U&RR CLEARANCE:

NO

24h. C&S CLEARANCE:

NO

24i. R/W CLEARANCE:

NO

24j. CUSTOMIZED SCHEDULE:

NO

24k. SCOPING DOCUMENT:

NO

**25. DESCRIPTION OF REQUEST**

Establish new project.

**26. JUSTIFICATION OF REQUEST**

Federally funded CMAQ project to assist in traffic congestion mitigation in the MAG region through the implementation of the Incident Response Unit. IRU will contribute to congestion mitigation through the operational efforts of rapid response to traffic incident management (TIM) and the removal of debris and disabled/abandoned vehicles that disrupt the normal flow of traffic. IRU worked with MAG to distribute the funds over three (3) years.

IRU Operational Costs/Staff: \$493K

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED****REQUESTED ACTIONS:**

ESTABLISH A NEW PROJECT

**APPROVED / RECOMMENDED ACTIONS:**
REQUEST APPROVED  
SUBJECT TO PPAC APPROVAL - 12/2/2020
**PRB APPROVED**

7. PPAC - PROJECT MODIFICATIONS AND NEW PROJECTS - DISCUSSION AND POSSIBLE ACTION

7-10	Route & MP:	Statewide
	Project Name:	STATEWIDE ITS MASTER PLAN
	Type of Work:	DEVELOP ITS MASTER PLAN
	County:	Statewide
	District:	Statewide
	Schedule:	
	Project:	M716201X TIP#: 102249
	Project Manager:	Susan Anderson
	Program Amount:	\$0
	New Program Amount:	\$350,000
	Requested Action:	Establish a new project.

---



**06**

1. PRB Meeting Date: 11/17/2020 ☒ 2. Teleconference: (602) 712-6910

3. Form Date / 5. Form By:

11/19/2020

Susan Anderson

4. Project Manager / Presenter:

Susan Anderson @ (602) 712-6910

1615 W Jackson St, 065R - 6003 SYSTEMS TECHNOLOGY

6. Project Name:

STATEWIDE ITS MASTER PLAN

7. Type of Work:

DEVELOP ITS MASTER PLAN

8. CPSID: 9. District: 10. Route: 11. County: 12. Beg MP: 13. TRACS #: 14. Len (Mi.): 15. Fed Id #:  
 - Phoenix Statewide M716201X ?

16. Program Budget: \$0

17. Program Item #: 102249

18. Current Approved Program Budget:

\$0

18a. (+/-) Program Budget Request:

\$350

18b Total Program Budget After Request:

\$350

**CURRENTLY APPROVED:****19. BUDGET ITEMS:****CHANGE / REQUEST:****19A. BUDGET ITEMS:**

Item #	Amount	Description	Comments
78821	\$350	TSM&O	

**CURRENT SCHEDULE:**

21. CURRENT FISCAL YEAR:

22. CURRENT BID READY:

23. CURRENT ADV DATE:

**CHANGE REQUEST/NEW SCHEDULE:**

21A. REQUEST FISCAL YEAR:

22A. REQUEST BID READY:

23A. REQUEST ADV DATE:

20. JPA #'s:

SIGNED:

NO

ADV:

NO

**PROJECT FUNDING VERIFIED BY PM**

**CHANGE IN:** 24a. PROJECT NAME: NO 24b. TYPE OF WORK: NO 24c. SCOPE: NO 24d. CURRENT STAGE: NOT APPLICABLE

24e. ENVIRONMENTAL CLEARANCE: NOT APPLICABLE

24f. MATERIALS MEMO COMP: NOT APPLICABLE

24g. U&amp;RR CLEARANCE: NOT APPLICABLE

24h. C&amp;S CLEARANCE: NOT APPLICABLE

24i. R/W CLEARANCE: NOT APPLICABLE

24j. CUSTOMIZED SCHEDULE: NOT APPLICABLE

24k. SCOPING DOCUMENT: NOT APPLICABLE

**25. DESCRIPTION OF REQUEST**

Establish a new project.

**26. JUSTIFICATION OF REQUEST**

The purpose of this project will be to procure a consultant to develop an ITS Master Plan for the TSMO Division. The ITS Master Plan will define the goals and objectives of ADOT's ITS systems in support of TSMO initiatives. This will allow for selection and prioritization of various initiatives and ITS deployments to meet TSMO's strategic goals. The Master Plan project will:

1. Provide high-level prioritization for the programmatic, geographic/physical, functional and IT requirements for expansion of ITS systems throughout the state.
2. Establish a strategic action plan for deployment of ITS technologies to address current and future initiatives. Evaluate strategies and develop an implementation roadmap.
3. Identify internal business processes, foundational components that are needed to advance initiatives and projects.
4. Summarize / Document the ITS Master Plan

Consultant = \$350K

**27. CONCERNS OF REQUEST****28. OTHER ALTERNATIVES CONSIDERED**

21

**REQUESTED ACTIONS:**

ESTABLISH A NEW PROJECT

**APPROVED / RECOMMENDED ACTIONS:**

REQUEST APPROVED  
 SUBJECT TO PPAC APPROVAL - 12/2/2020

**PRB APPROVED**

## **8. FUTURE MEETINGS**

Listed below are the next regularly scheduled meetings of the Priority Planning Advisory Committee (PPAC). Meetings will be held in the ADOT Board Room, however, times, dates, and location may change and will be announced at the time of the distribution of the agenda.

- December 30th, 2020 10:00am Wednesday
- February 3, 2021 10:00am Wednesday
- March 3, 2021 10:00am Wednesday
- March 31, 2021 10:00am Wednesday
- May 5, 2021 10:00am Wednesday
- June 2, 2021 10:00am Wednesday
- June 30, 2021 10:00am Wednesday
- August 4, 2021 10:00am Wednesday
- September 1, 2021 10:00am Wednesday
- September 29, 2021 10:00am Wednesday
- November 3, 2021 10:00am Wednesday
- December 1, 2021 10:00am Wednesday

## **9. ADJOURN PRIORITY PLANNING ADVISORY COMMITTEE MEETING**

**DRAFT MINUTES FOR THE  
ARIZONA DEPARTMENT OF TRANSPORTATION  
PRIORITY PLANNING ADVISORY COMMITTEE  
Mary Peters Conference Room  
206 South 17th Avenue, Phoenix, AZ 85007  
Wednesday November 4, 2020 @ 10:00AM**

The meeting of the Priority Planning Advisory Committee (PPAC) was held on Wednesday November 4, 2020 @ 10:00AM with Chairman Dallas Hammit presiding.

Other committee members were present as follows:

Steve Boschen, Brent Cain, Elise Maza was voting for Kristine Ward, Clemenc Ligocki, Barry Crockett, Tim Tait (Non-Voting), Don Kriz, and John Morales was voting for Tim Lane.

**1. CALL TO ORDER**

Chairman Hammit called the Priority Planning Advisory Committee meeting to order at 10:00AM.

**2. ROLL CALL**

Lynn Sugiyama conducted a roll call of the committee members. Greg Byres was absent and unable to chair the meeting and Dallas Hammit agreed to chair this PPAC Meeting. A quorum was present.

**3. TITLE VI OF THE CIVIL RIGHTS ACT OF 1964, AS AMENDED**

Chairman Hammit asked if any persons from the public were at the meeting. There was no comment made. Chairman Byres stated that in accordance to the Title VI Civil Rights Act of 1964, and the Americans with Disabilities Act, ADOT will not discriminate on the basis of race, color, national origin, age, sex, or disability. If accommodations are requested, the public may contact someone on the PPAC Committee or the Civil Rights Office at 602-712-8964.

**4. CALL TO THE AUDIENCE**

Chairman Hammit requested a Call to the Audience for any comments or issues to be addressed, There were no comments from the public.

**5. APPROVAL OF PPAC MINUTES FROM THE 9/30/2020 MEETING**

The minutes from the PPAC meeting held on 9/30/2020 were approved.

**Chairman Hammit called for a motion to approve the PPAC minutes from the meeting on 9/30/2020. Steve Boschen made a motion to approve.**

**Don Kriz seconded the motion. The motion Motion carried unanimously.**

**6. PROGRAM MONITORING REPORT**

The Program Monitoring Report was distributed to the Committee. There were no comments.

**2021-2025 TRANSPORTATION FACILITIES CONSTRUCTION:  
DISCUSSION AND POSSIBLE ACTION ON PROGRAM & PROJECT MODIFICATIONS**

7-1	<b>Route &amp; MP:</b>	I-10 @ MP 90
	<b>Project Name:</b>	443rd Ave - E of Wintersburg Rd
	<b>Type of Work:</b>	PAVEMENT REHABILITATION
	<b>County:</b>	Maricopa
	<b>District:</b>	Southwest
	<b>Schedule:</b>	
	<b>Project:</b>	F034501D TIP#: 101684
	<b>Project Manager:</b>	Jennifer Acuna
	<b>Program Amount:</b>	\$0
	<b>New Program Amount:</b>	\$416,000
	<b>Requested Action:</b>	Establish new project. Change project name.

---

Item 7-1 was presented by: Madhav Mundle  
Chairman called for a motion to approve Item 7-1.  
Steve Boschen made the motion to approve.  
Clemenc Ligocki seconded the motion. Motion carried unanimously.

Discussion followed that the project in the Tentative FY 2021-2025 Five Year Transportation Facilities Construction Program was named W of Salome Rd - W of Tonapah (F034501D). However, Yuma District wanted to change the project name to 443rd Ave - E of Wintersburg Rd (F034501D) prior to the approval of the Final FY 2021-2025 Five Year Transportation Facilities Construction Program. Now that the FY 2021-2025 Five year Transportation Facilities Construction Program has been approved with the name change, it was agreed that the project can be approved as PPAC Only and does not need further approval from the State Transportation Board. Steve Boschen and Clem Ligocki amended their motion. PRB will be corrected to show W of Salome Rd - W of Tonapah to reflect the former name. Motion passed.

---

---

7-2                    **Route & MP:**            I-40 @ MP 186  
                         **Project Name:**        TRANSWESTERN RD - COSNINO RD  
                         **Type of Work:**        VARIABLE SPEED LIMIT SIGNS & SUPPORTING ITS INFRASTRUCTURE  
                         **County:**                Coconino  
                         **District:**               Northcentral  
                         **Schedule:**  
                         **Project:**                F028101D TIP#: 100997  
                         **Project Manager:**    Michael Andazola  
                         **Program Amount:**     \$563,000  
                         **New Program Amount:** \$637,000  
                         **Requested Action:**    Increase design budget,Change scope, Change Project Name.

---

**Item 7-2 was presented by: Michael Andazola**  
**Chairman called for a motion to approve Item 7-2.**  
**Brent Cain made the motion to approve.**  
**Steve Boschen seconded the motion. Motion carried unanimously.**

---

---

7-3                    **Route & MP:**            Local Route  
                         **Project Name:**        STOCKTON HILL RD;FOUNTAIN HILLS RD-W CEDAR CANYON DR  
                         **Type of Work:**        RUMBLE STRIPS (CENTER AND EDGELINE)  
                         **County:**                Mohave  
                         **District:**  
                         **Schedule:**  
                         **Project:**                T027101D TIP#: 100500  
                         **Project Manager:**    Michael Andazola  
                         **Program Amount:**     \$0  
                         **New Program Amount:** \$170,000  
                         **Requested Action:**    Establish Project

---

**Item 7-3 was presented by: Michael Andazola**  
**Chairman called for a motion to approve Item 7-3.**  
**Don Kriz made the motion to approve.**  
**Steve Boschen seconded the motion. Motion carried unanimously.**

---

---

7-4                    **Route & MP:**                    US 60 @ MP 227.7  
                         **Project Name:**                    QUEEN CREEK BRIDGE  
                         **Type of Work:**                    CONSTRUCT BRIDGE REPLACEMENT  
                         **County:**                    Pinal  
                         **District:**                    Southeast  
                         **Schedule:**  
                         **Project:**                    H856601D TIP#: 100975  
                         **Project Manager:**                    Tafwachi Katapa  
                         **Program Amount:**                    \$1,200,000  
                         **New Program Amount:**                    \$1,971,000  
                         **Requested Action:**                    Increase Budget.

---

**Item 7-4 was presented by: Tricia Brown**  
**Chairman called for a motion to approve Item 7-4.**  
**Steve Boschen made the motion to approve.**  
**Don Kriz seconded the motion. Motion carried unanimously.**

---

---

7-5                    **Route & MP:**                    SR 73 @ MP 348.0  
                         **Project Name:**                    POST OFFICE CANYON BRIDGE  
                         **Type of Work:**                    CONSTRUCT BRIDGE REHABILITATION  
                         **County:**                    Navajo  
                         **District:**                    Northeast  
                         **Schedule:**                    FY 2020  
                         **Project:**                    F010901C TIP#: 8810  
                         **Project Manager:**                    Tricia Brown  
                         **Program Amount:**                    \$2,500,000  
                         **New Program Amount:**                    \$3,000,000  
                         **Requested Action:**                    Increase budget.  
                            Change bid advertisement date.

---

**Item 7-5 was presented by: Tricia Brown**  
**Chairman called for a motion to approve Item 7-5.**  
**Steve Boschen made the motion to approve.**  
**Barry Crockett seconded the motion. Motion carried unanimously**

---

---

## **8. FUTURE MEETINGS**

Listed below are the next regularly scheduled meetings of the Priority Planning Advisory Committee (PPAC). Meetings will be held in the ADOT Board Room, however, times, dates, and location may change and will be announced at the time of the distribution of the agenda.

December 30th, 2020 on Wednesday at 10am.  
February 3, 2021 on Wednesday at 10am.  
March 3, 2021 on Wednesday at 10am.  
March 31, 2021 on Wednesday at 10am.  
May 5, 2021 on Wednesday at 10am.  
June 2, 2021 on Wednesday at 10am.  
June 30, 2021 on Wednesday at 10am.  
August 4, 2021 on Wednesday at 10am.  
September 1, 2021 on Wednesday at 10am.  
September 29, 2021 on Wednesday at 10am.  
November 3, 2021 on Wednesday at 10am.  
December 1, 2021 on Wednesday at 10am.

## **9. ADJOURN PRIORITY PLANNING ADVISORY COMMITTEE MEETING**

Chairman Dallas Hammit announced the motion to adjourn the meeting.  
Meeting adjourned at 10:18am

---
