New DCR Template (Pre-Design) | Program and Project Management Section | 11-Apr-2012 03:02 PM

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
Area for Schedules Not Yet Published		346.0d	346.0d	09-Apr-2012 08:00 AM	05-Aug-2013 05:00 PM	0.0d
Templates from our website		346.0d	346.0d	09-Apr-2012 08:00 AM	05-Aug-2013 05:0...	0.0d
New DCR Template (Pre-Design)		346.0d	346.0d	09-Apr-2012 08:00 AM	05-Aug-2013 05:0...	0.0d
2X00	Scoping Request Rcvd-Assigned to Scoping Leader	20.0d	20.0d	09-Apr-2012 08:00 AM	04-May-2012 05:0...	0.0d
2D10	Notice to Proceed	1.0d	1.0d	07-May-2012 08:00 AM	07-May-2012 05:0...	0.0d
2D20	Scoping meeting	10.0d	10.0d	08-May-2012 08:00 AM	21-May-2012 05:0...	0.0d
2D30	Consultants prepare technical reports	75.0d	75.0d	22-May-2012 08:00 AM	03-Sep-2012 05:0...	0.0d
2D40	Prepare Init. DCR for Draft Review	120.0d	120.0d	04-Sep-2012 08:00 AM	18-Feb-2013 05:0...	0.0d
2D42	Prepare Draft EA for Draft Review	120.0d	120.0d	04-Sep-2012 08:00 AM	18-Feb-2013 05:0...	0.0d
2D50	Distribute Init. DCR for review & comments	30.0d	30.0d	19-Feb-2013 08:00 AM	01-Apr-2013 05:00...	0.0d
2D60	Public hearing	45.0d	45.0d	02-Apr-2013 08:00 AM	03-Jun-2013 05:00...	0.0d
2D70	Prepare final environmental document	20.0d	20.0d	04-Jun-2013 08:00 AM	01-Jul-2013 05:00 ...	0.0d
2D80	Prepare final DCR	20.0d	20.0d	02-Jul-2013 08:00 AM	29-Jul-2013 05:00 ...	0.0d
2D90	Distribute final DCR	5.0d	5.0d	30-Jul-2013 08:00 AM	05-Aug-2013 05:0...	0.0d
2D92	Distribute final EA	5.0d	5.0d	30-Jul-2013 08:00 AM	05-Aug-2013 05:0...	0.0d
PD999	PRE-DESIGN COMPLETE	0.0d	0.0d		05-Aug-2013 05:0...	0.0d

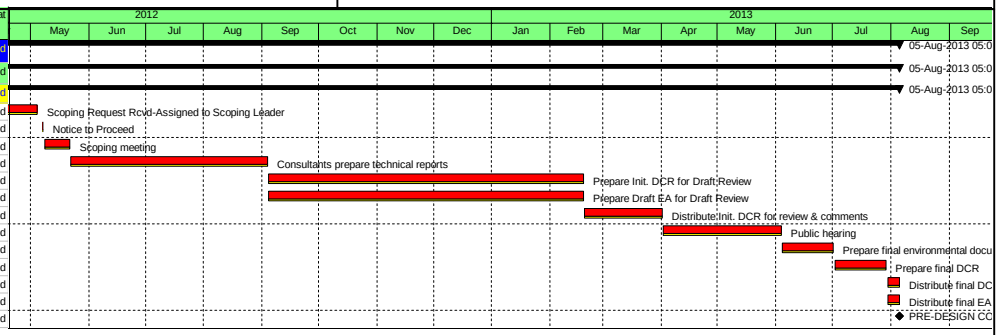

Primary Baseline | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.
